


The Structural Spine of DCOS


System Mechanics, Governance
& Operational Rules

"In DCOS, the Work Breakdown Structure is not a scheduling artefact. It is the primary location and control structure of the entire platform."

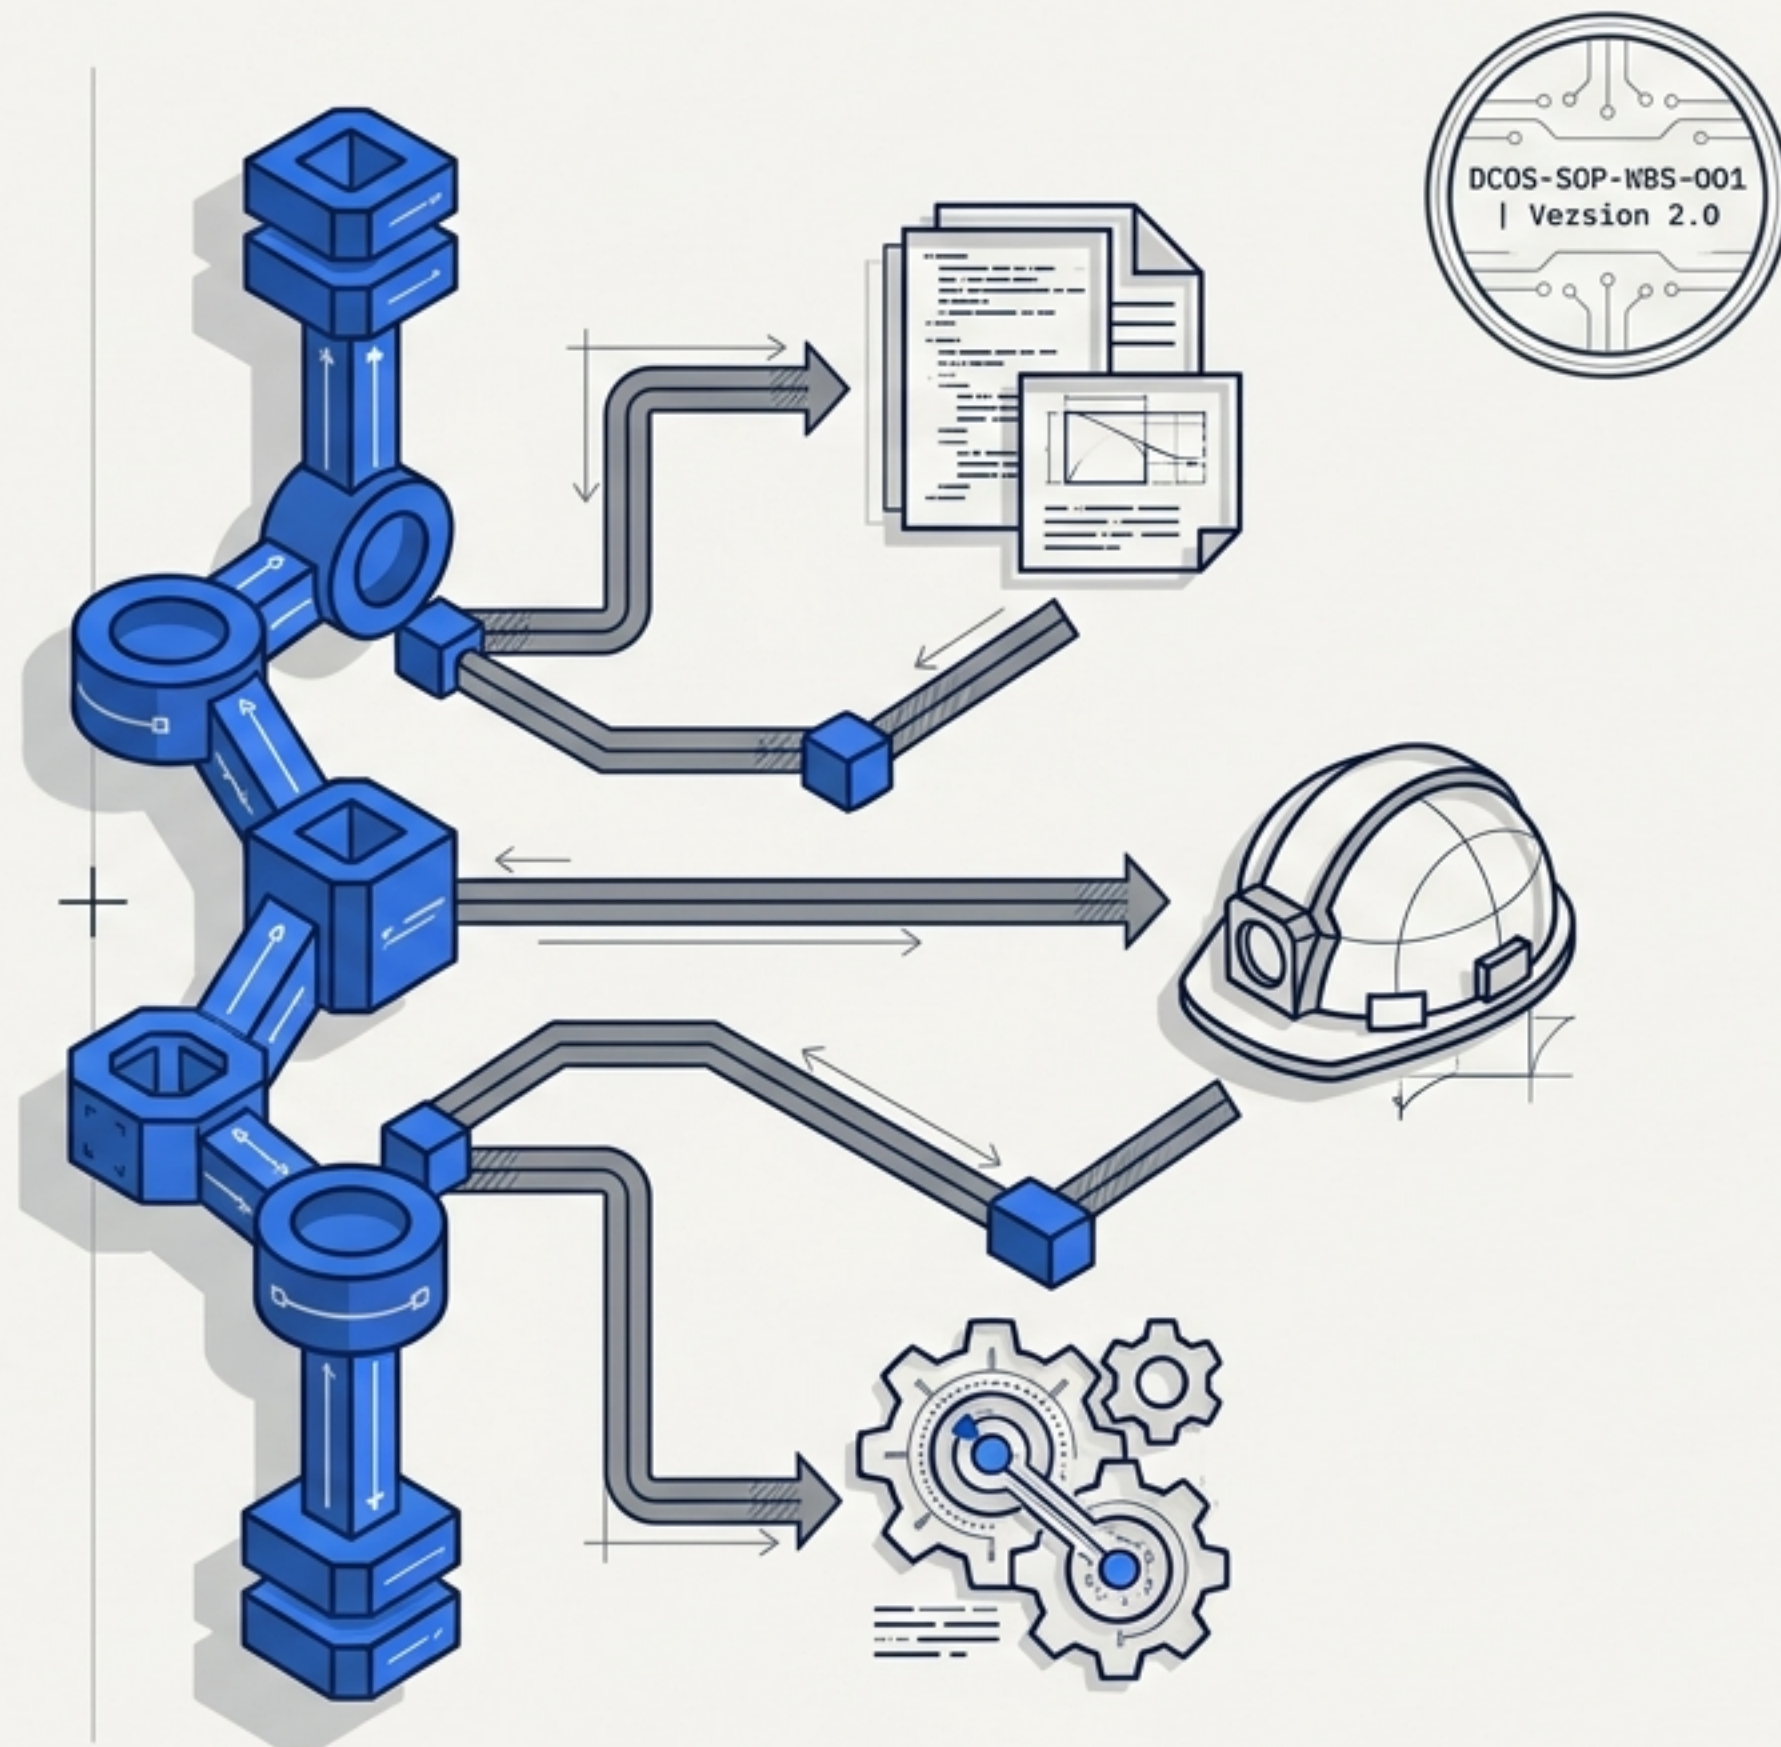

The Prime Directive: Everything Belongs to a Location

No task, document, cost, or incident may exist in DCOS without a valid WBS reference. This is non-negotiable.

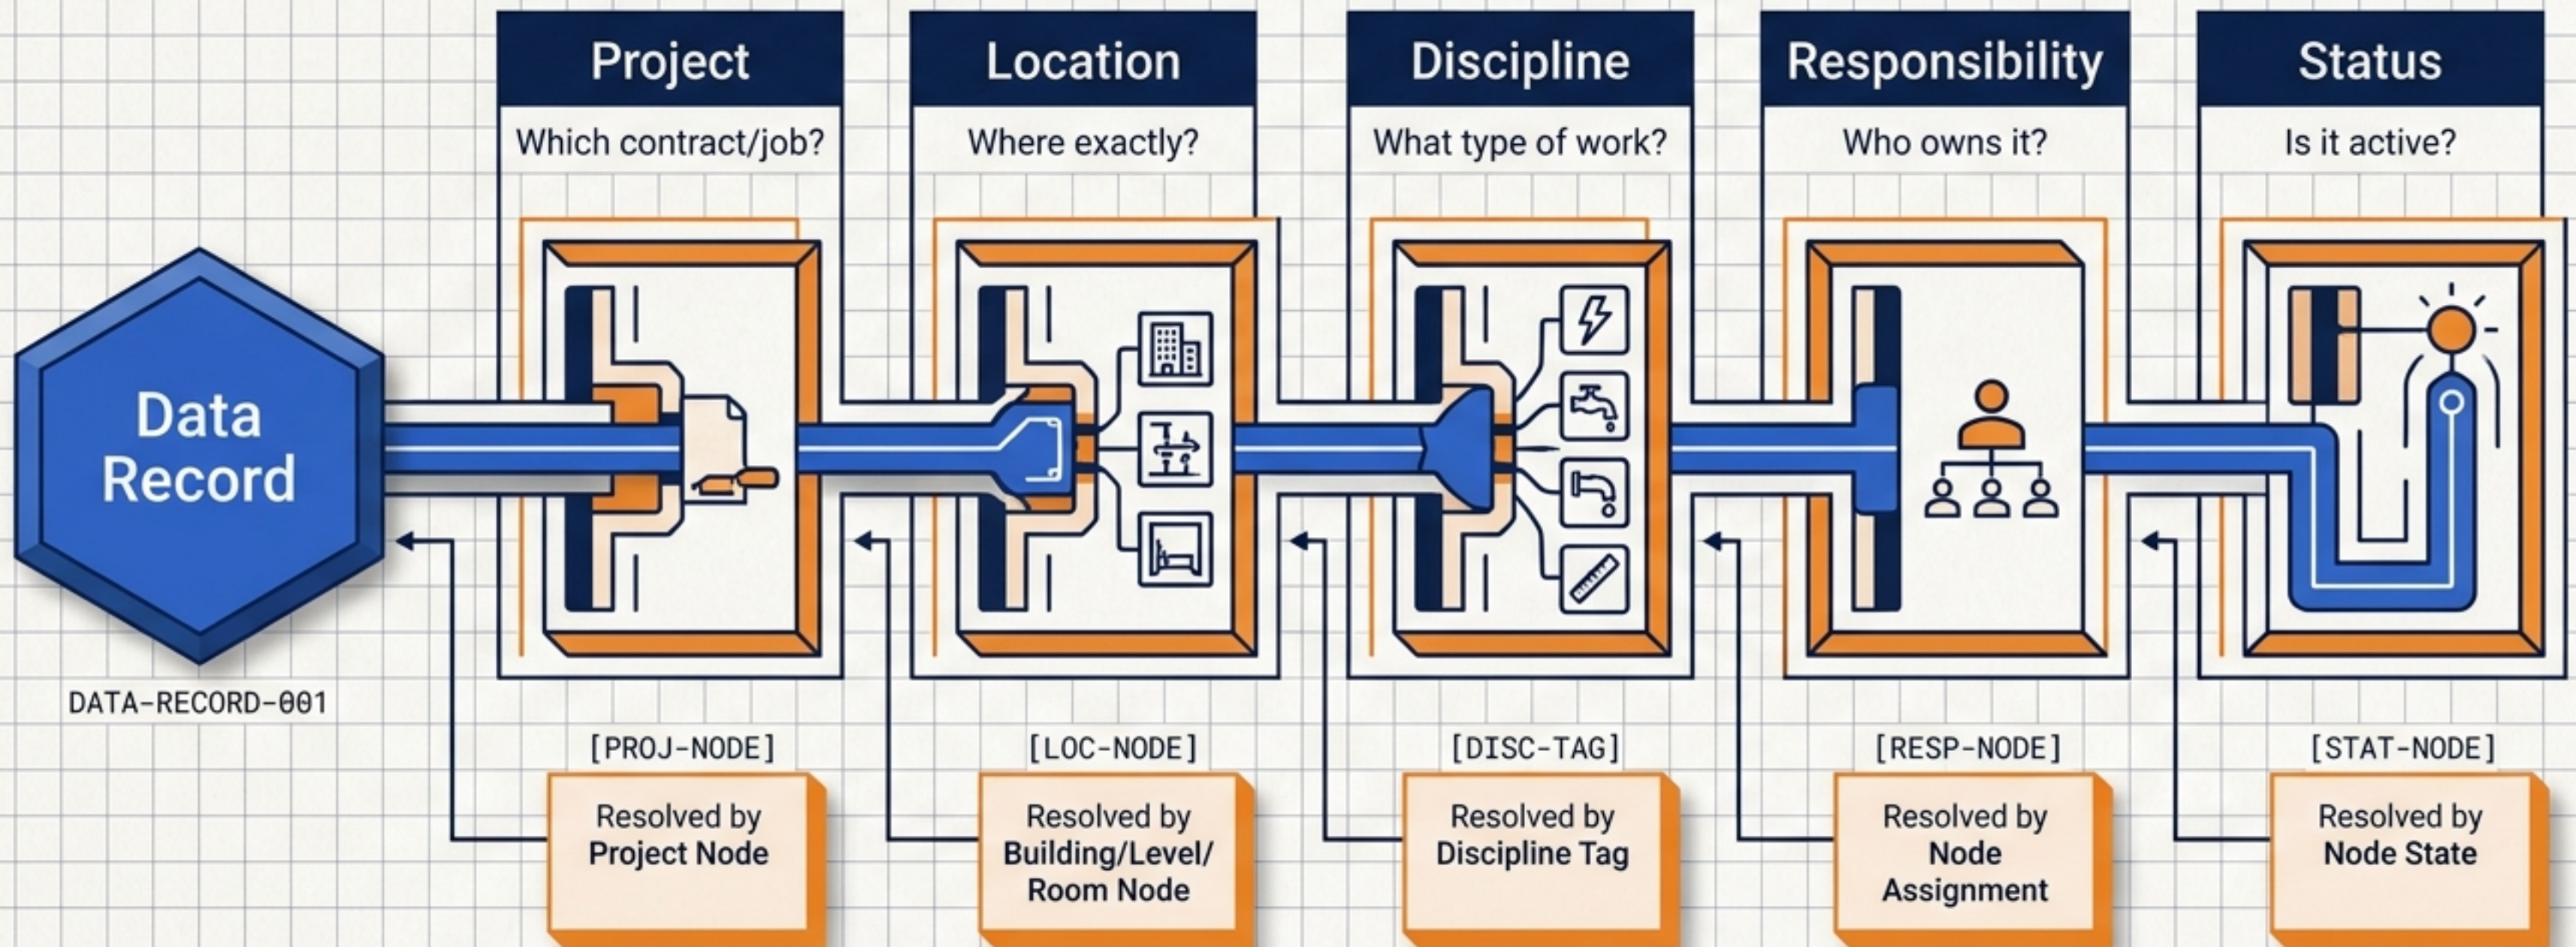


The Standard 7-Level Anatomy

Level 6 | Task: [PROJ-NODE]
Executable unit of work attached to a Leaf Node (e.g., Install Rebar).

Level 4 | Room: [LOC-NODE]
Functional space (e.g., Meeting Room, Lobby).

Level 2 | Level: [LOC-NODE]
Vertical division (e.g., L05, Basement 2).

Level 0 | Project: [PROJ-NODE]
The top-level container (e.g., GDT Office Tower).

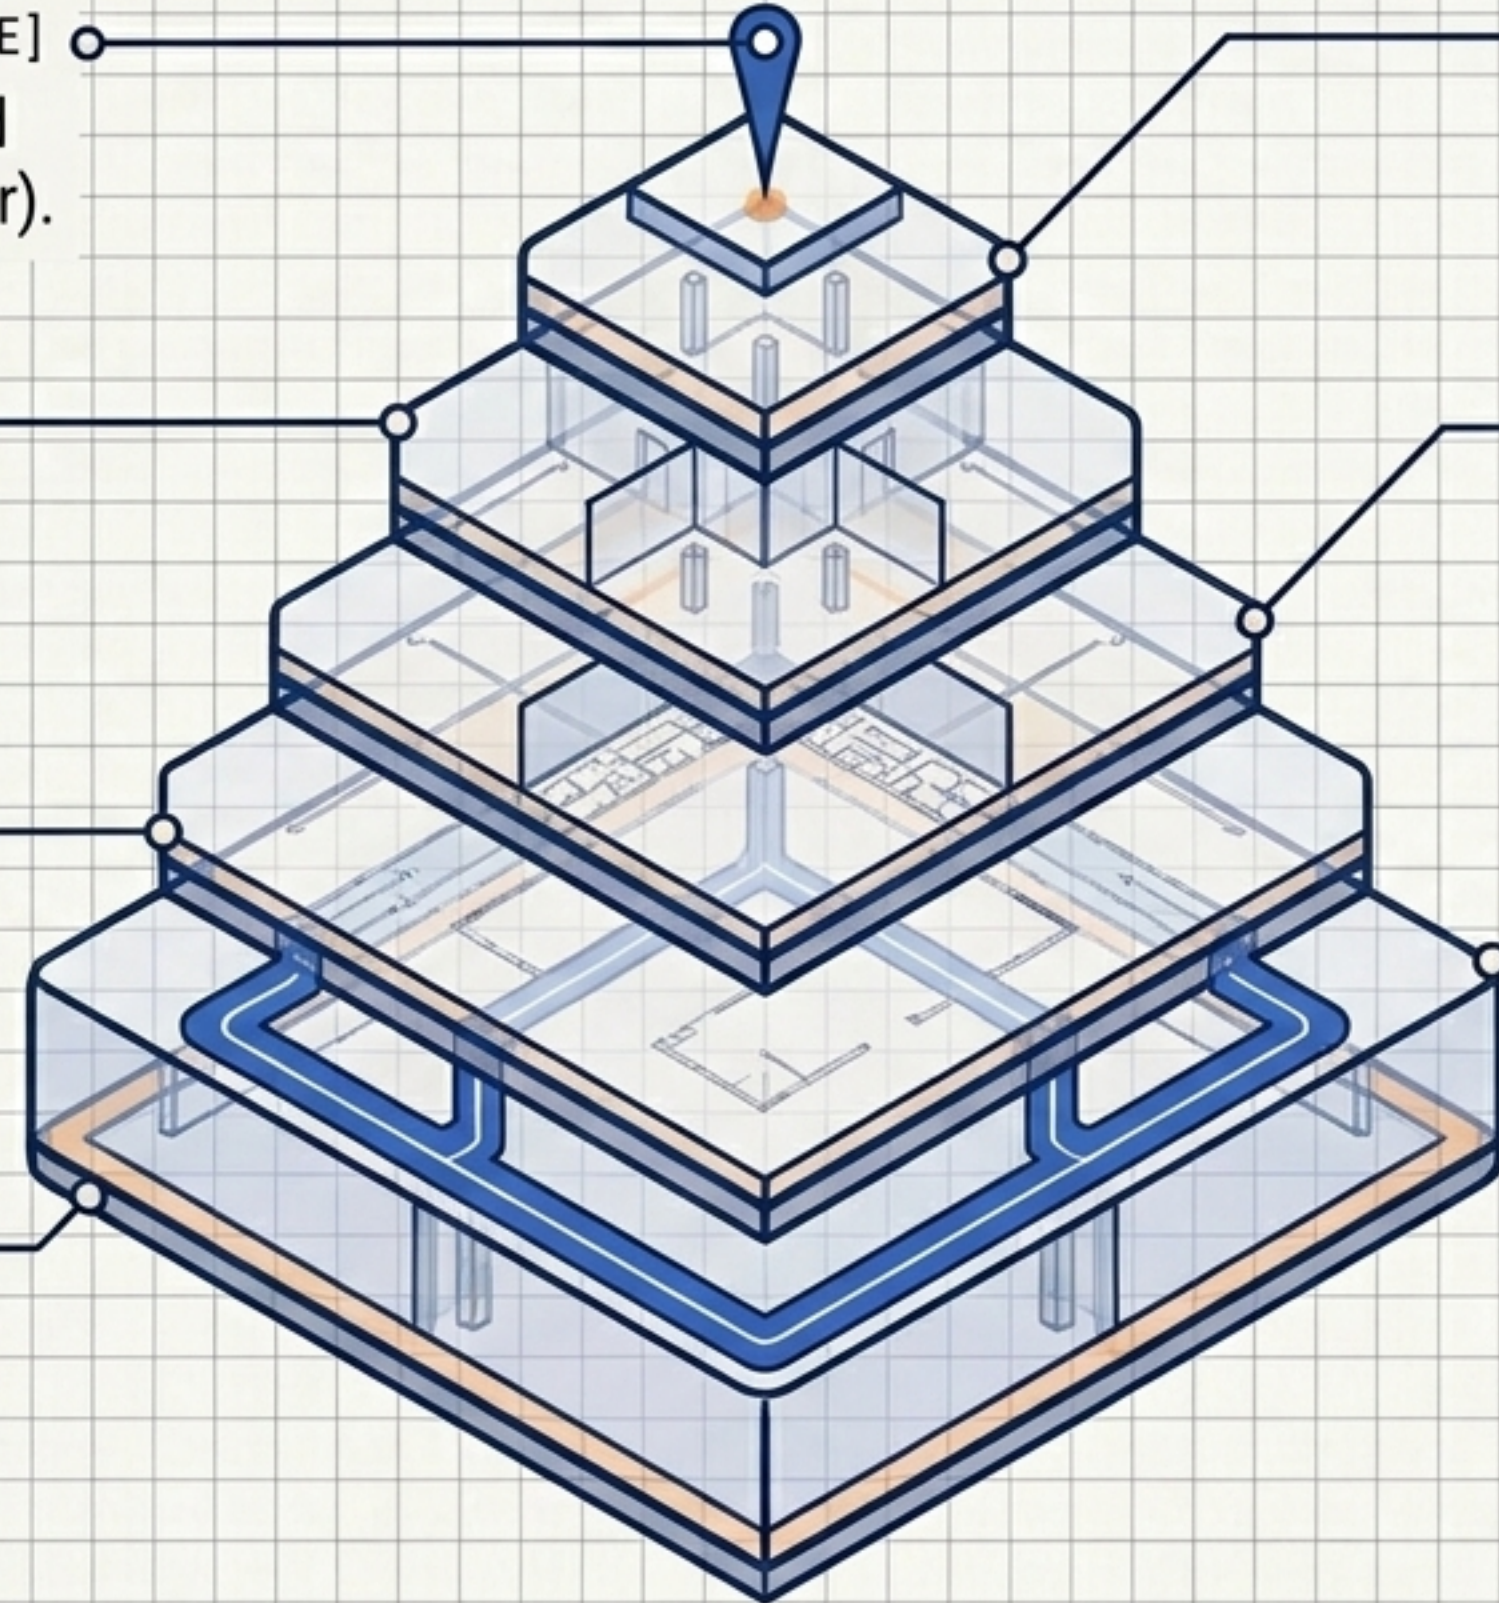

Level 5 | Element: [DEC-TAG]
Physical work component (e.g., Slab, Column).

Level 3 | Zone: [DISC-TAG]
Horizontal subdivision (e.g., Zone A, Zone B).


Level 1 | Building: [PODIUM]
Major division (e.g., Tower A, Podium).

Axiom: Always attach tasks to the Leaf Node (Level 6).


Dynamic Depth Adapts to the Asset

The Rule of Depth: The hierarchy must adapt to the physical reality of the project. Skip levels where they do not apply, but never skip a level merely for speed.

Dynamic Structure Matrix

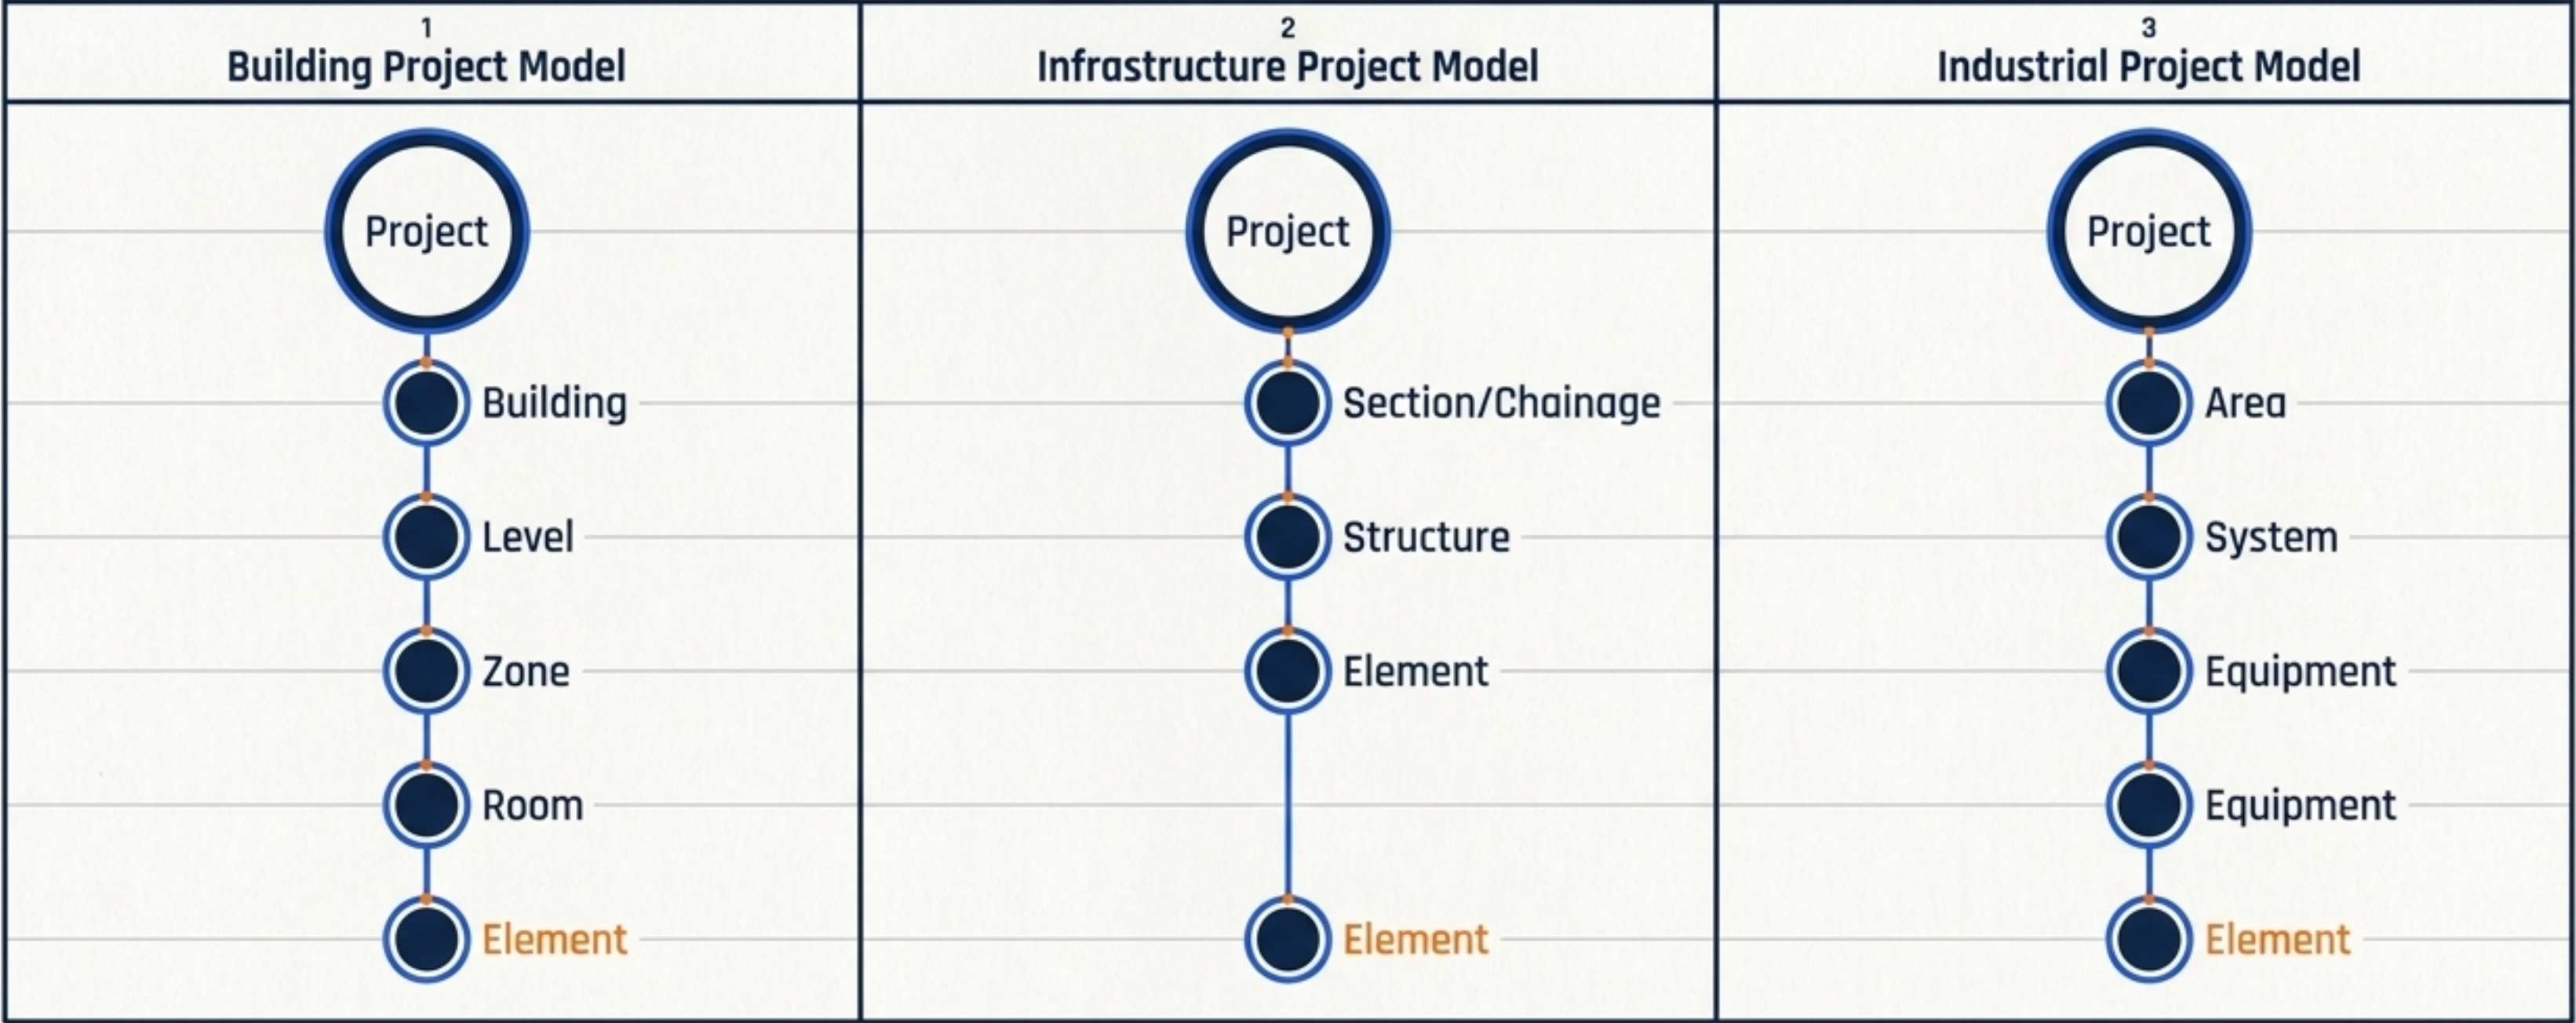

The DNA of a Node: Building the Full Path

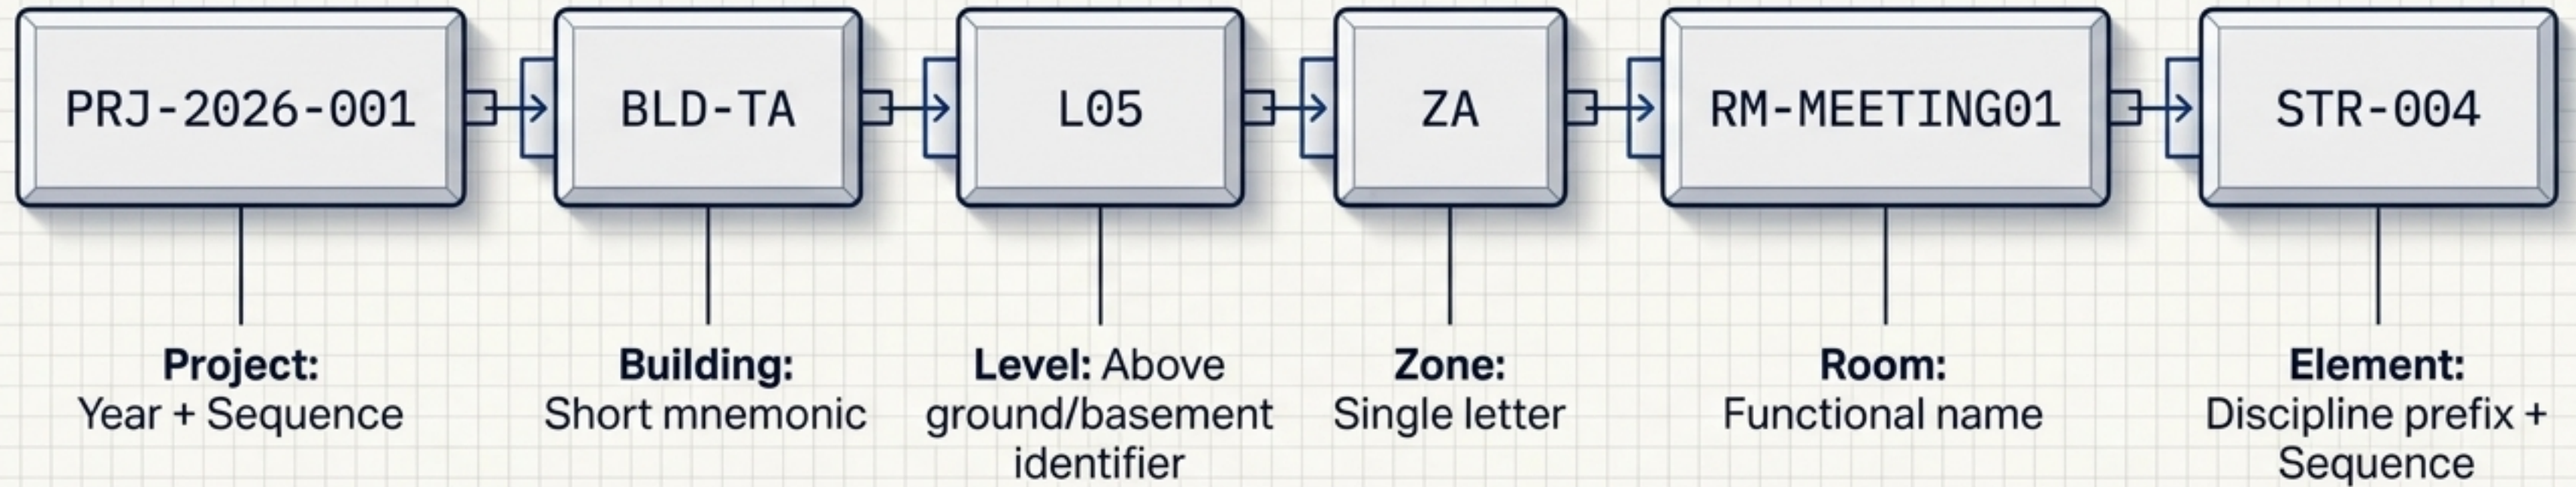


Resolved Path

PRJ-2026-001 · BLD-TA · L05 · ZA · RM-MEETING01 · STR-004

Governance Note: Codes must be **unique** within a project. Once a node is **Active** and carries records, its code is locked.


The Operating System Ecosystem

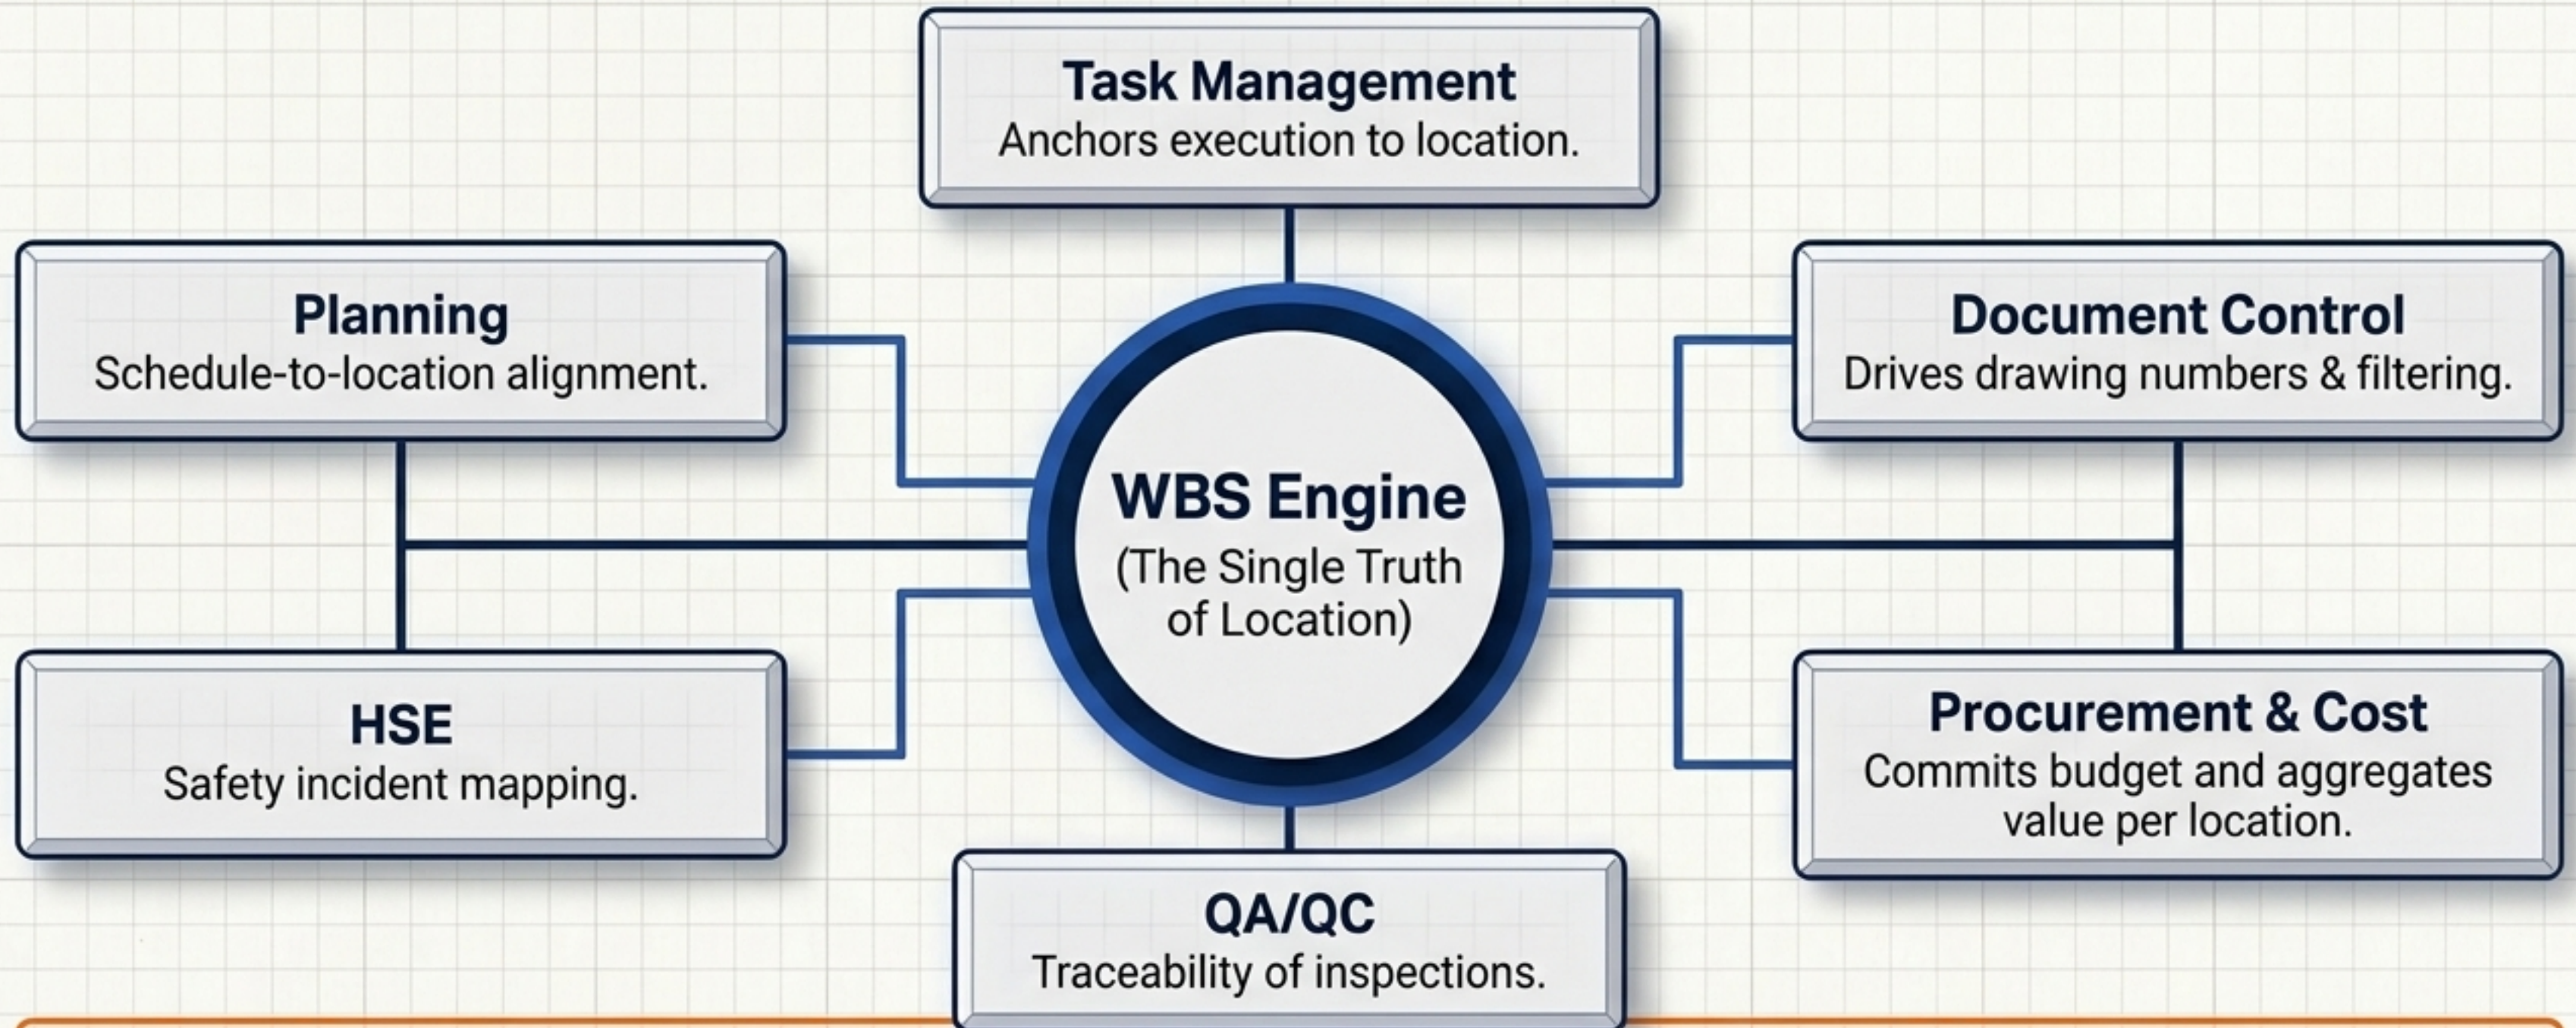

The Golden Rule: Modules must never create independent location structures. All modules consume WBS from the centralized engine.


Progress Aggregation: Upward Roll-Up

The Engine Rule: Progress is entered at the leaf (task) level only.
A parent's value is always derived, never entered directly.

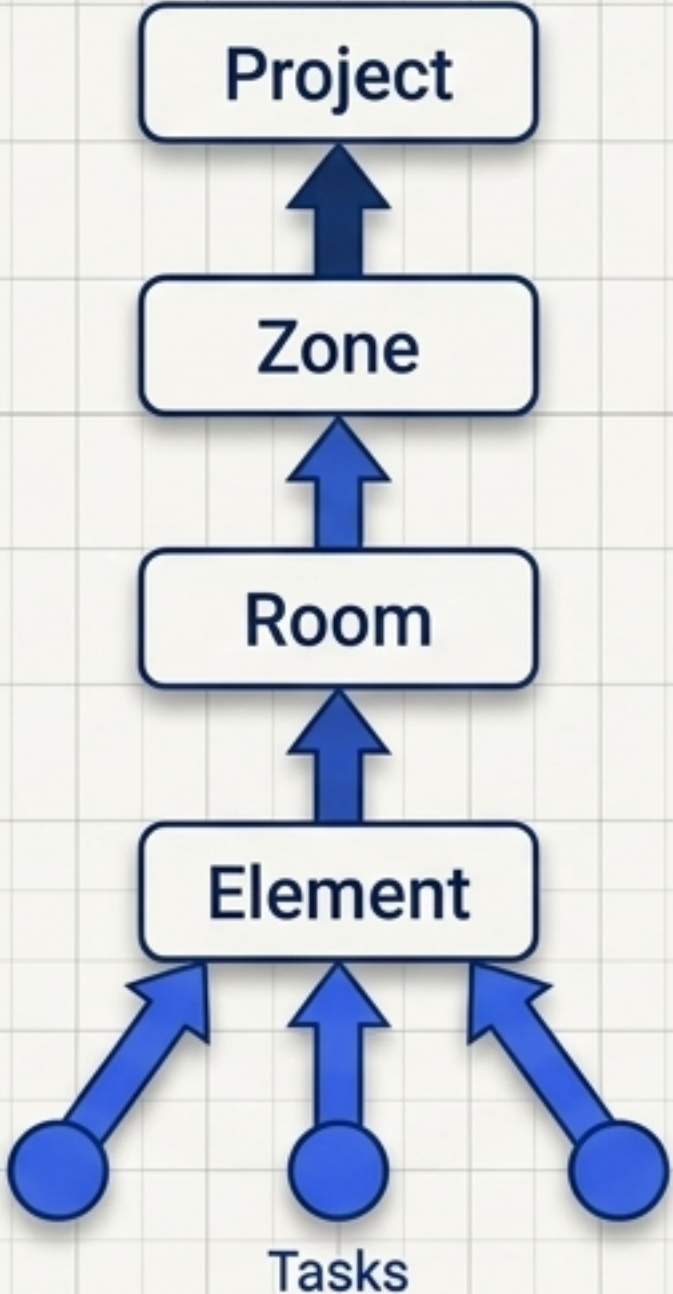

Progress Roll-up Matrix	
Simple Roll-Up	Weighted Roll-Up (Focuses on cost/effort reality)
Task 1: 100%	Slab pour (Weight 70, 100% done) = 70.0
Task 2: 50%	Door install (Weight 10, 0% done) = 0.0
Task 3: 0%	Wall finish (Weight 20, 50% done) = 10.0
Average = 50% Element Progress	Total Weighted = 80% Progress


The Assembly Line: Top-Down Creation

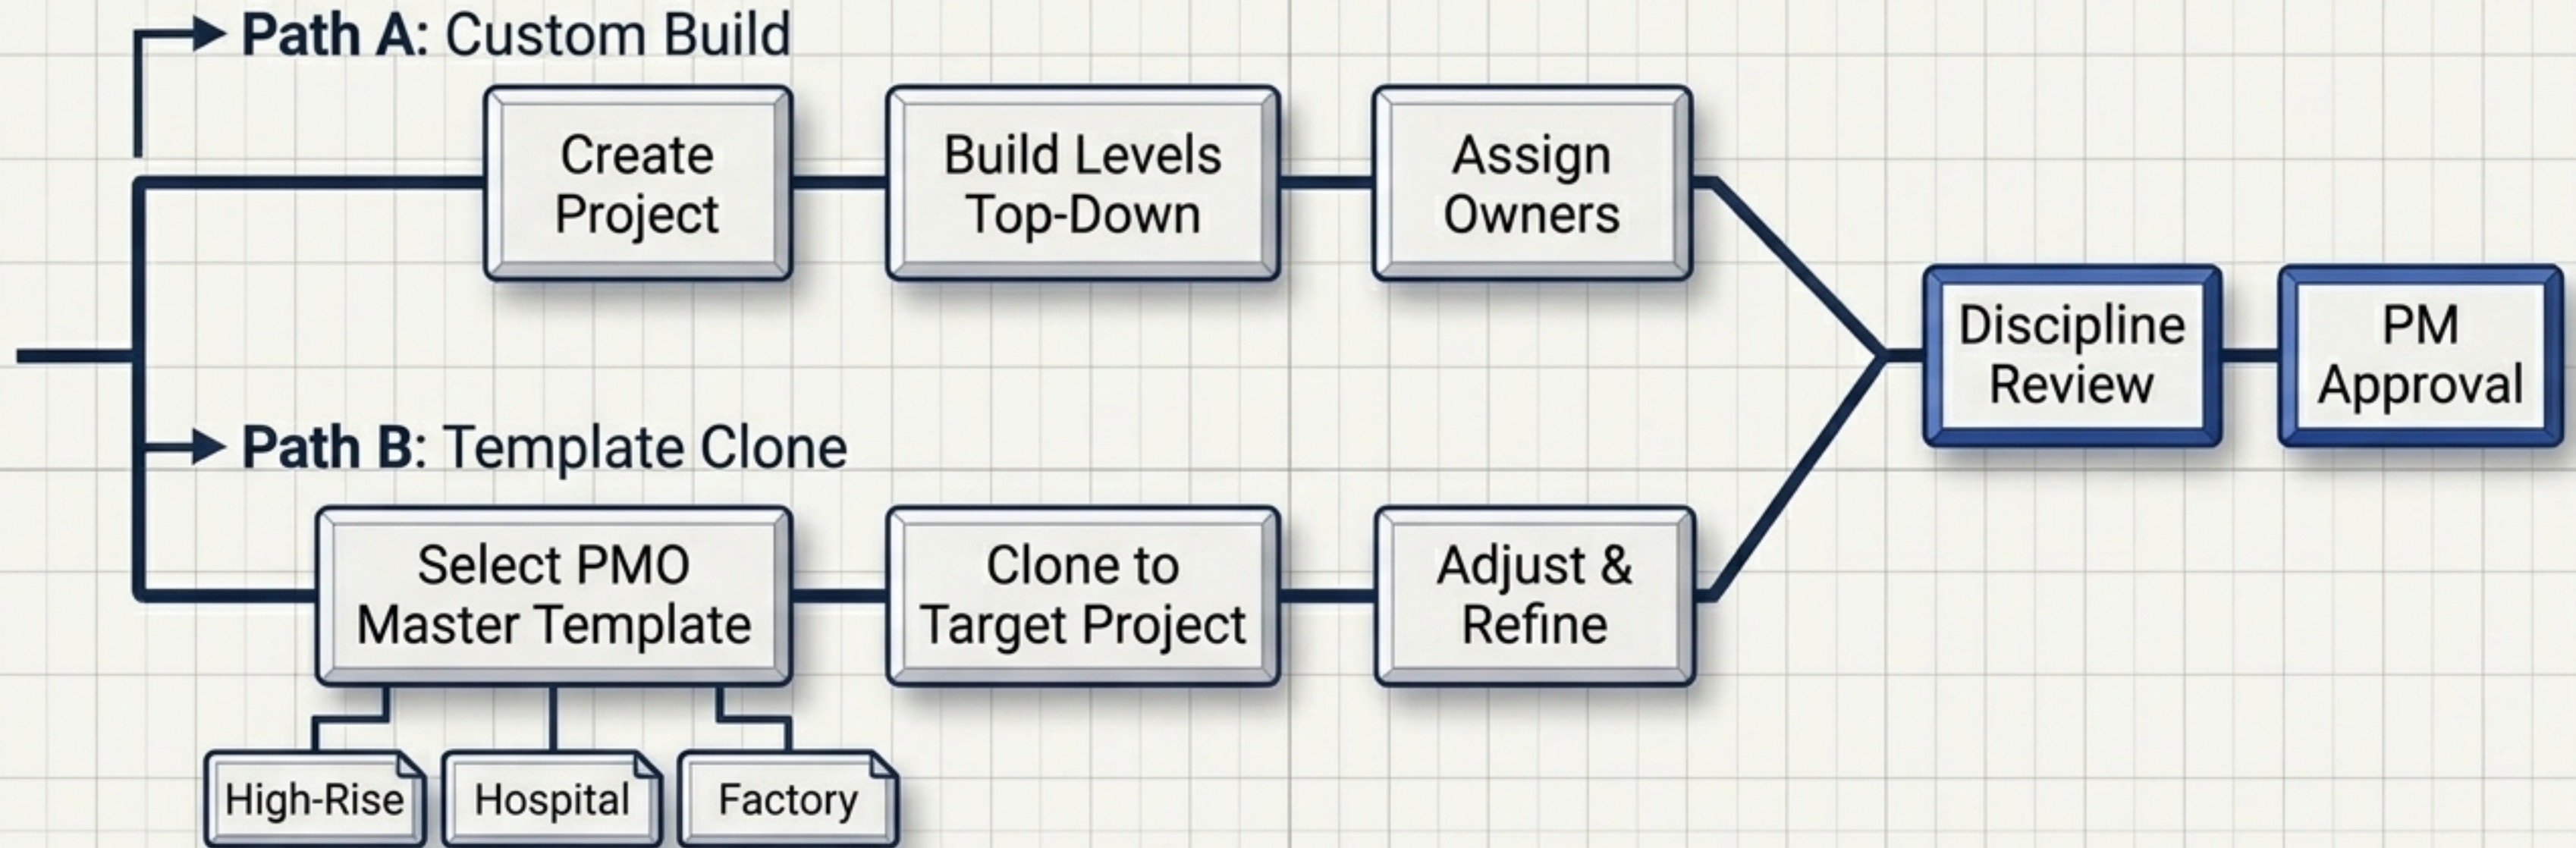

Template Governance: Templates are PMO-controlled master data. Project teams clone and adjust, but cannot edit the masters.

Checkpoints and the State Model

Transition Control: Only the Project Manager may approve Active → Closed and reopen Closed nodes.

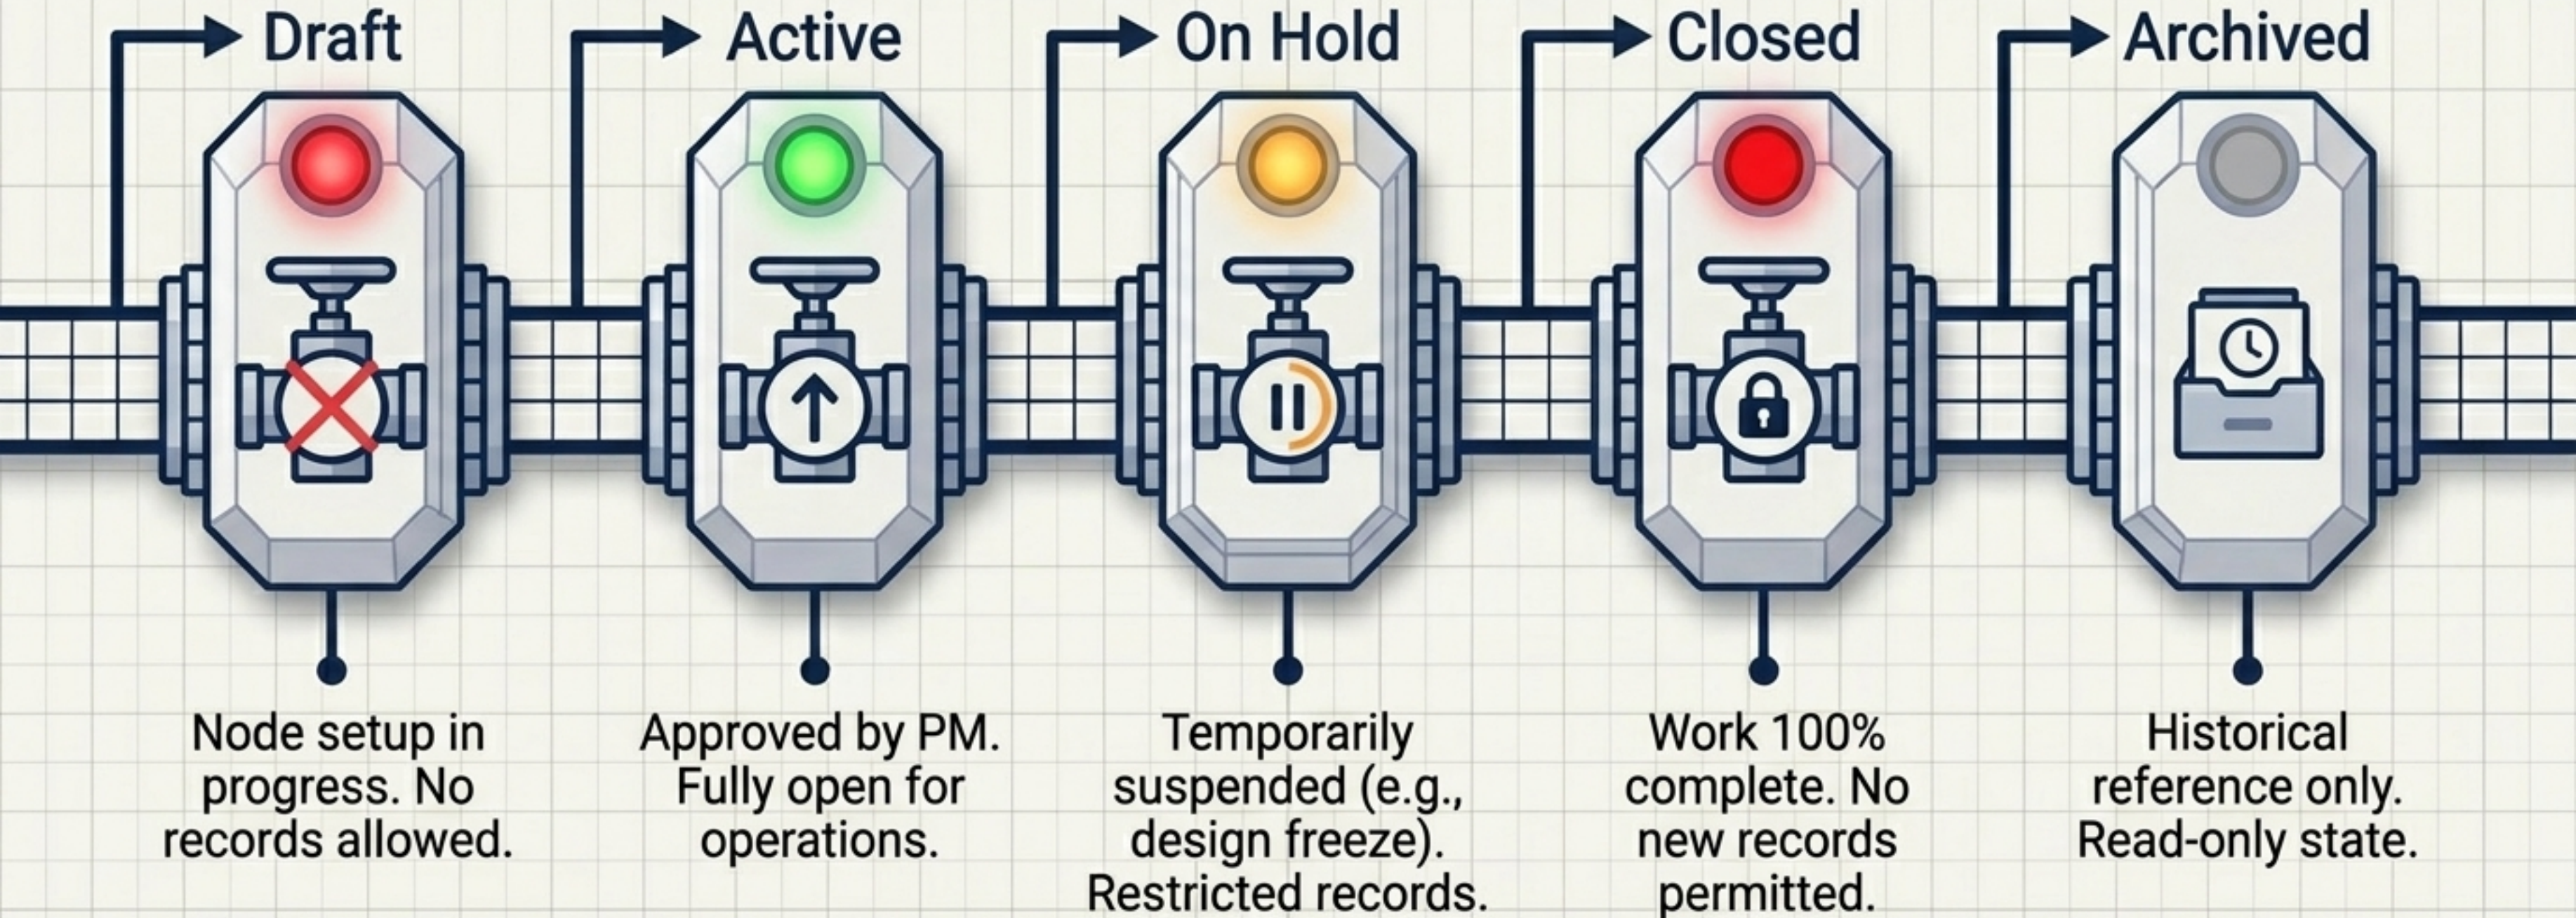

The Guardians of the Structure



PMO Manager (The Standard Bearer)

- Owns the overarching standard, templates, and cross-project consistency rules.



Project Manager (The Approver)

- Authorizes project activation, approves restricted structural changes, and owns the execution structure.



WBS Coordinator (The Builder)

- Performs day-to-day top-down building, updates descriptions, and applies approved changes.



Discipline Manager (The Reviewer)

- Confirms discipline tagging, verifies node ownership, and ensures the structure serves physical reality.

Note on inheritance: Child nodes inherit the owner and discipline of their parent automatically unless explicitly overridden.

The Shield: Change Control Rules

Integrity Rule: A node that carries live records is protected. It cannot be silently re-coded or deleted.

Change Control Matrix

Allowed Changes (No approval required)



Edit node description/name.



Change node owner/assignment
(logged + notified).



Add new child nodes.

Restricted Changes (PM/Admin Approval Required)



Change an Active WBS code.



Move a historical node
(with linked records).



Delete an existing node
(Admin technical delete only).


The Vault: Audit Trails and Archiving

The Append-Only Engine

Every structural action (Create, Edit, Activate, Move, Assign) is logged. Audit logs cannot be edited or deleted by any user, including administrators.

Audit Footprint

Captures **Who** (Snapshot of name/ID), **What** (Action type & Before/After values), and **When** (Timestamp).

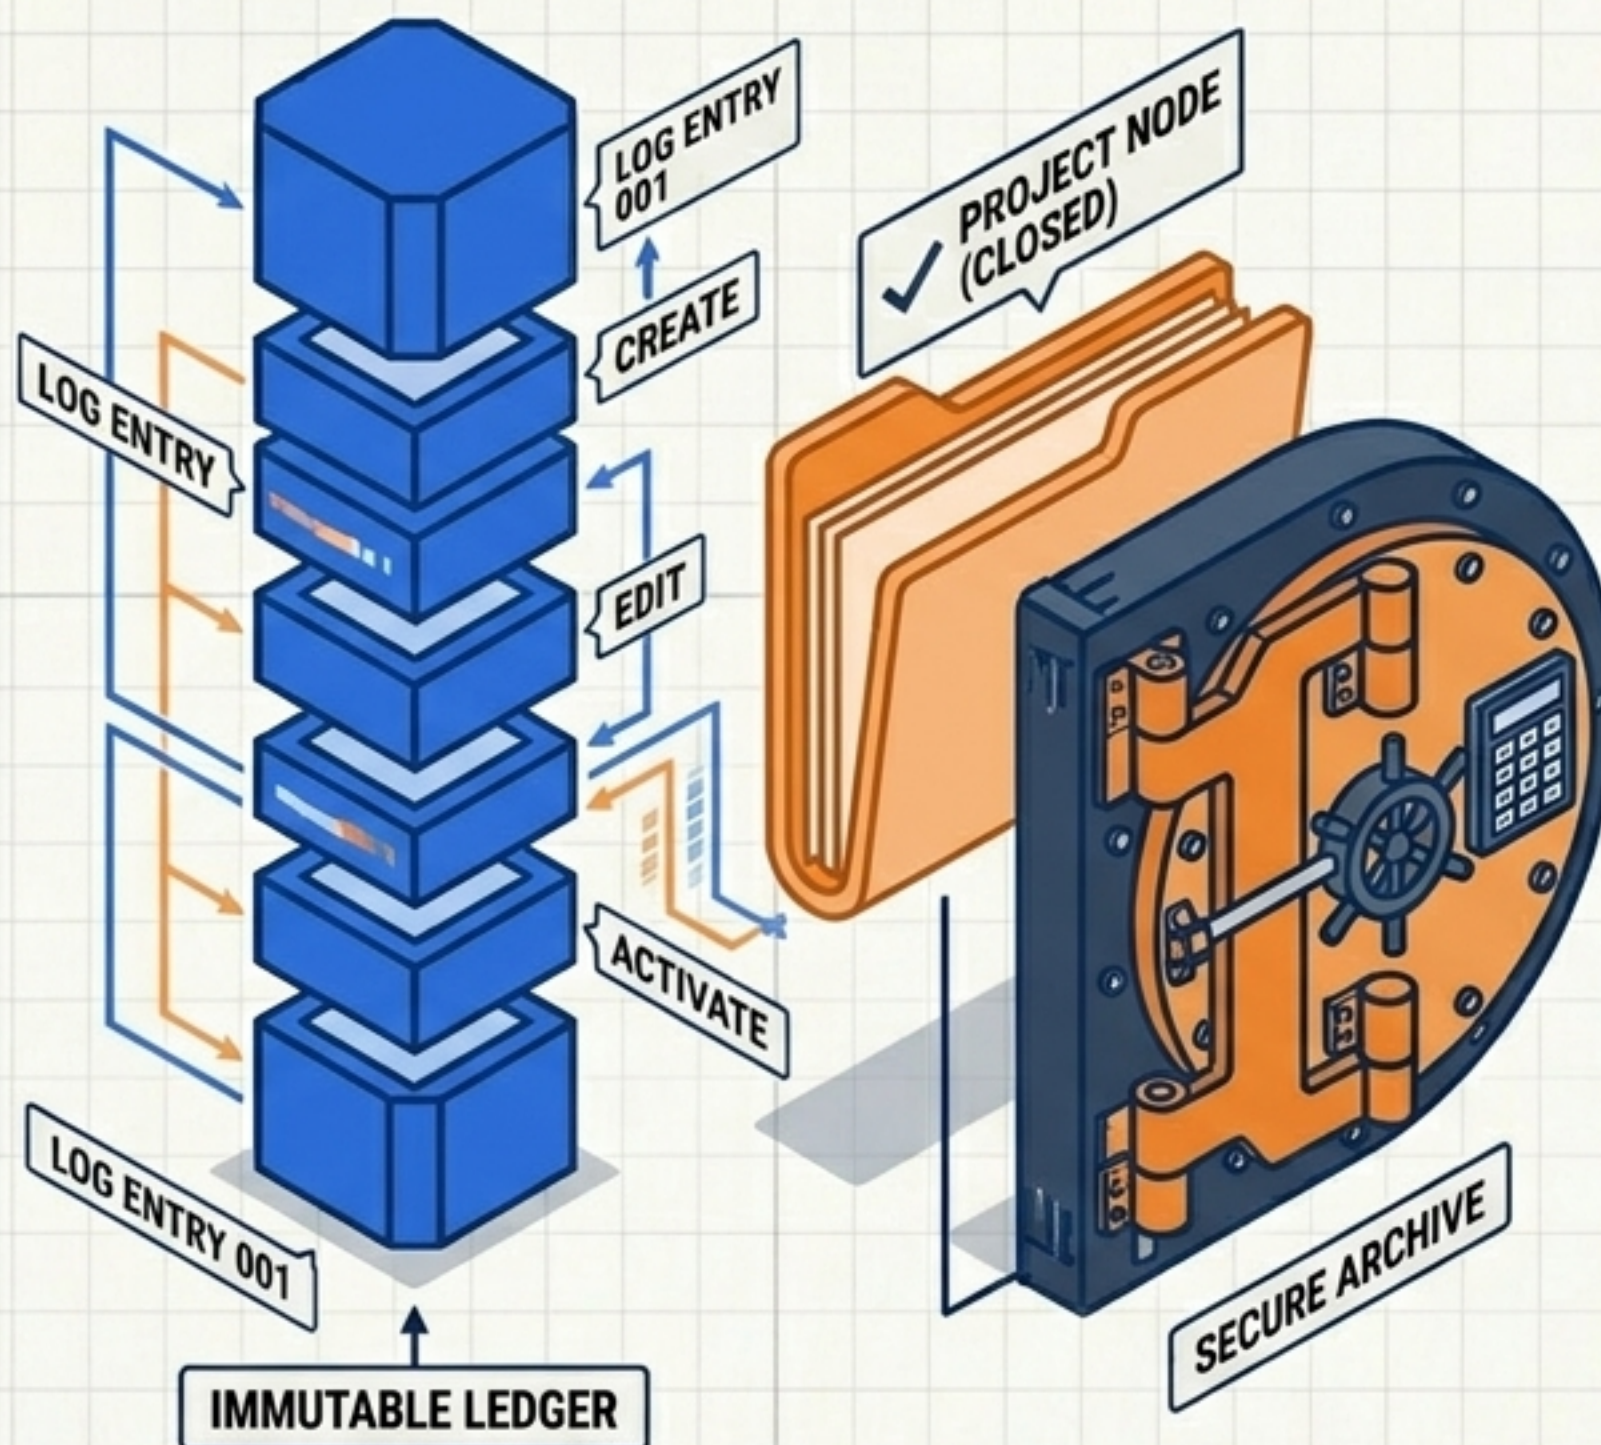

End of Life

(Closure Preconditions)

To close a node, all tasks must be closed, inspections passed, documents issued, and rolled-up progress at 100%.

Retention

Active WBS data remains in hot storage for duration + 2 years, before transitioning to warm/cold storage.

System Guardrails & Non-Conformances

The Orphan Task

Creating tasks without a WBS link. (Breaks traceability and roll-up).

ERROR: NO PARENT LINK

The Skipped Floor

Skipping the Zone level on a multi-zone layout. (Loses necessary location granularity).

ERROR: ZONE SKIPPED

The Duplicate

Reusing WBS codes. (Corrupts numbering & reporting).

ERROR: DUPLICATE WBS

The Discipline Mashup


Mixing disciplines into the physical hierarchy rather than using tags. (Confuses structure with discipline).

ERROR: HIERARCHY POLLUTION


The Top-Down Override

Entering progress manually at a parent node. (Bypasses roll-up integrity and mathematical logic).

ERROR: MANUAL OVERRIDE DETECTED

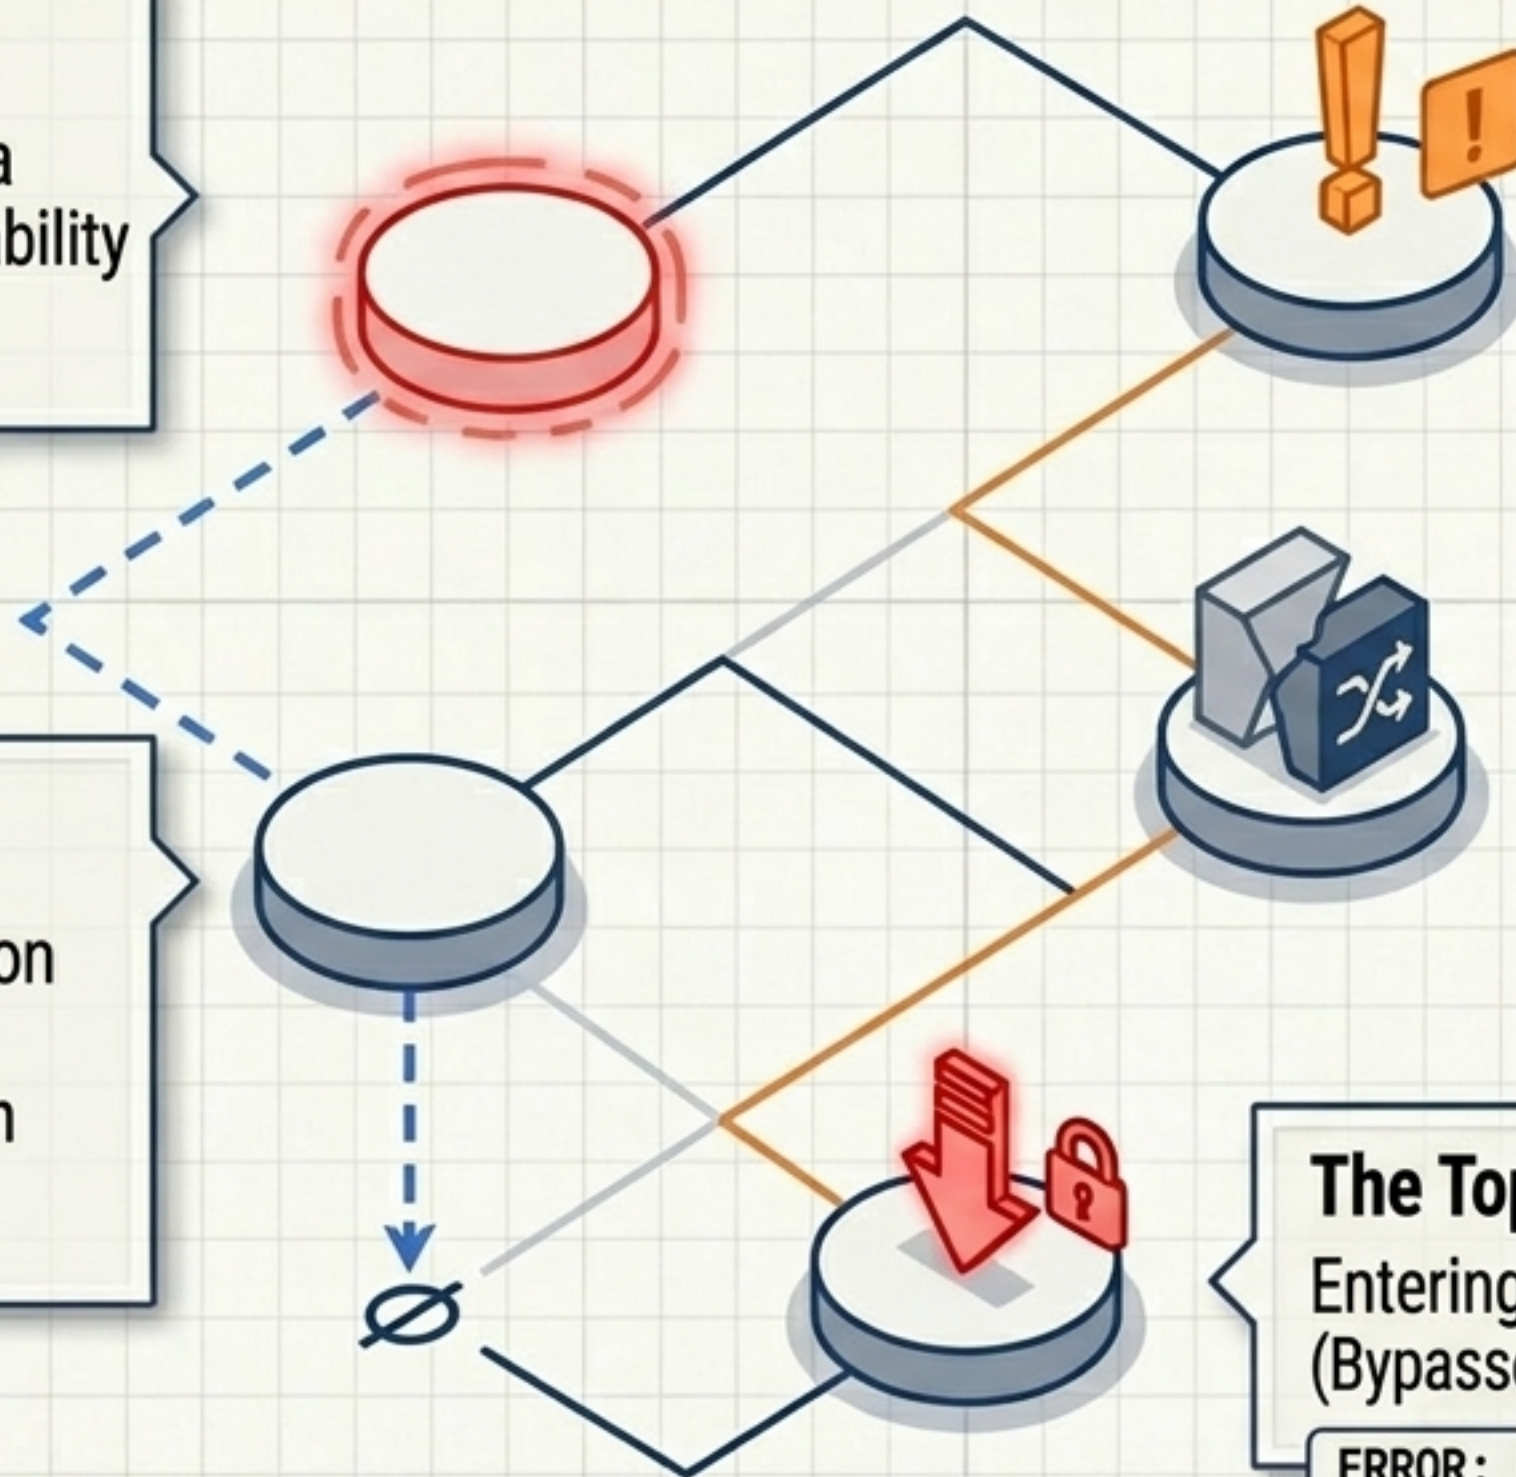

The Definition of Done

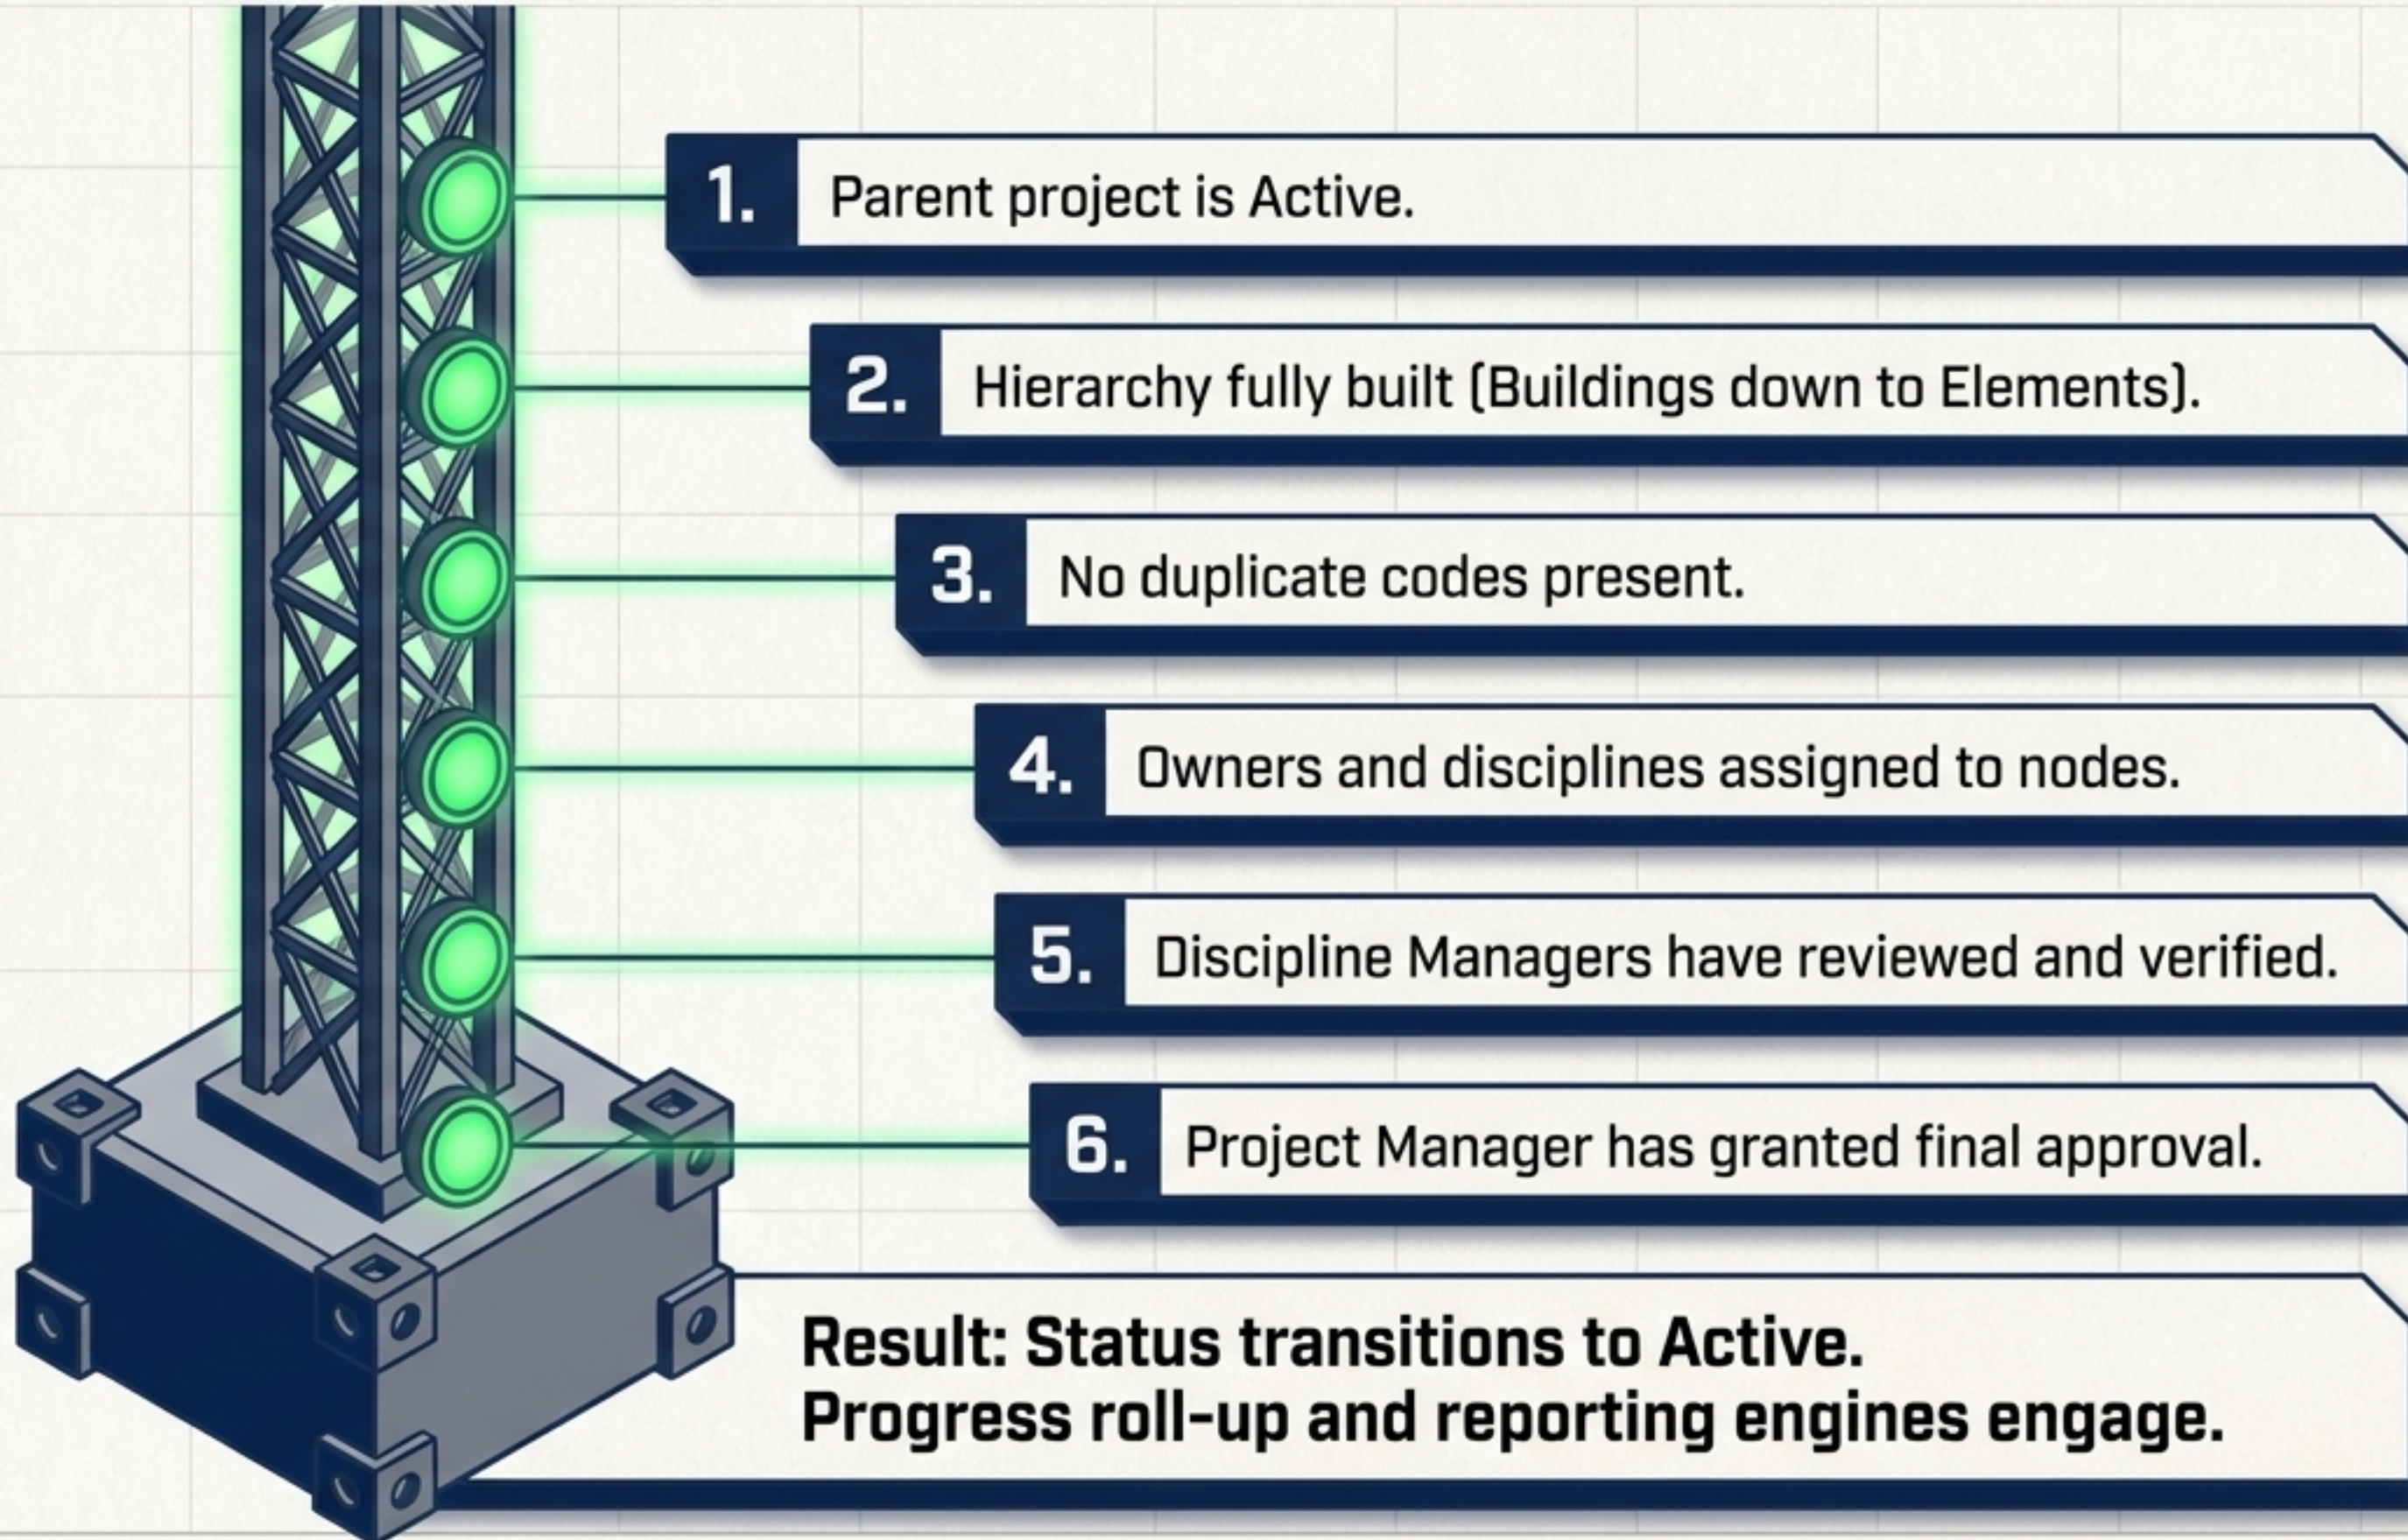

The Core Mandate

Tasks execute work.

Documents store information.

Costs track money.

**But the WBS provides the structure
that connects them all.**

Every project. Every location. Every task. Every document.

Must belong to a controlled WBS structure.

Without WBS, there is no project control.
