



DCOS Foundation: Project Setup & Activation

Architecting Control, Governance,
and Scalability in the Digital
Construction Operating System.

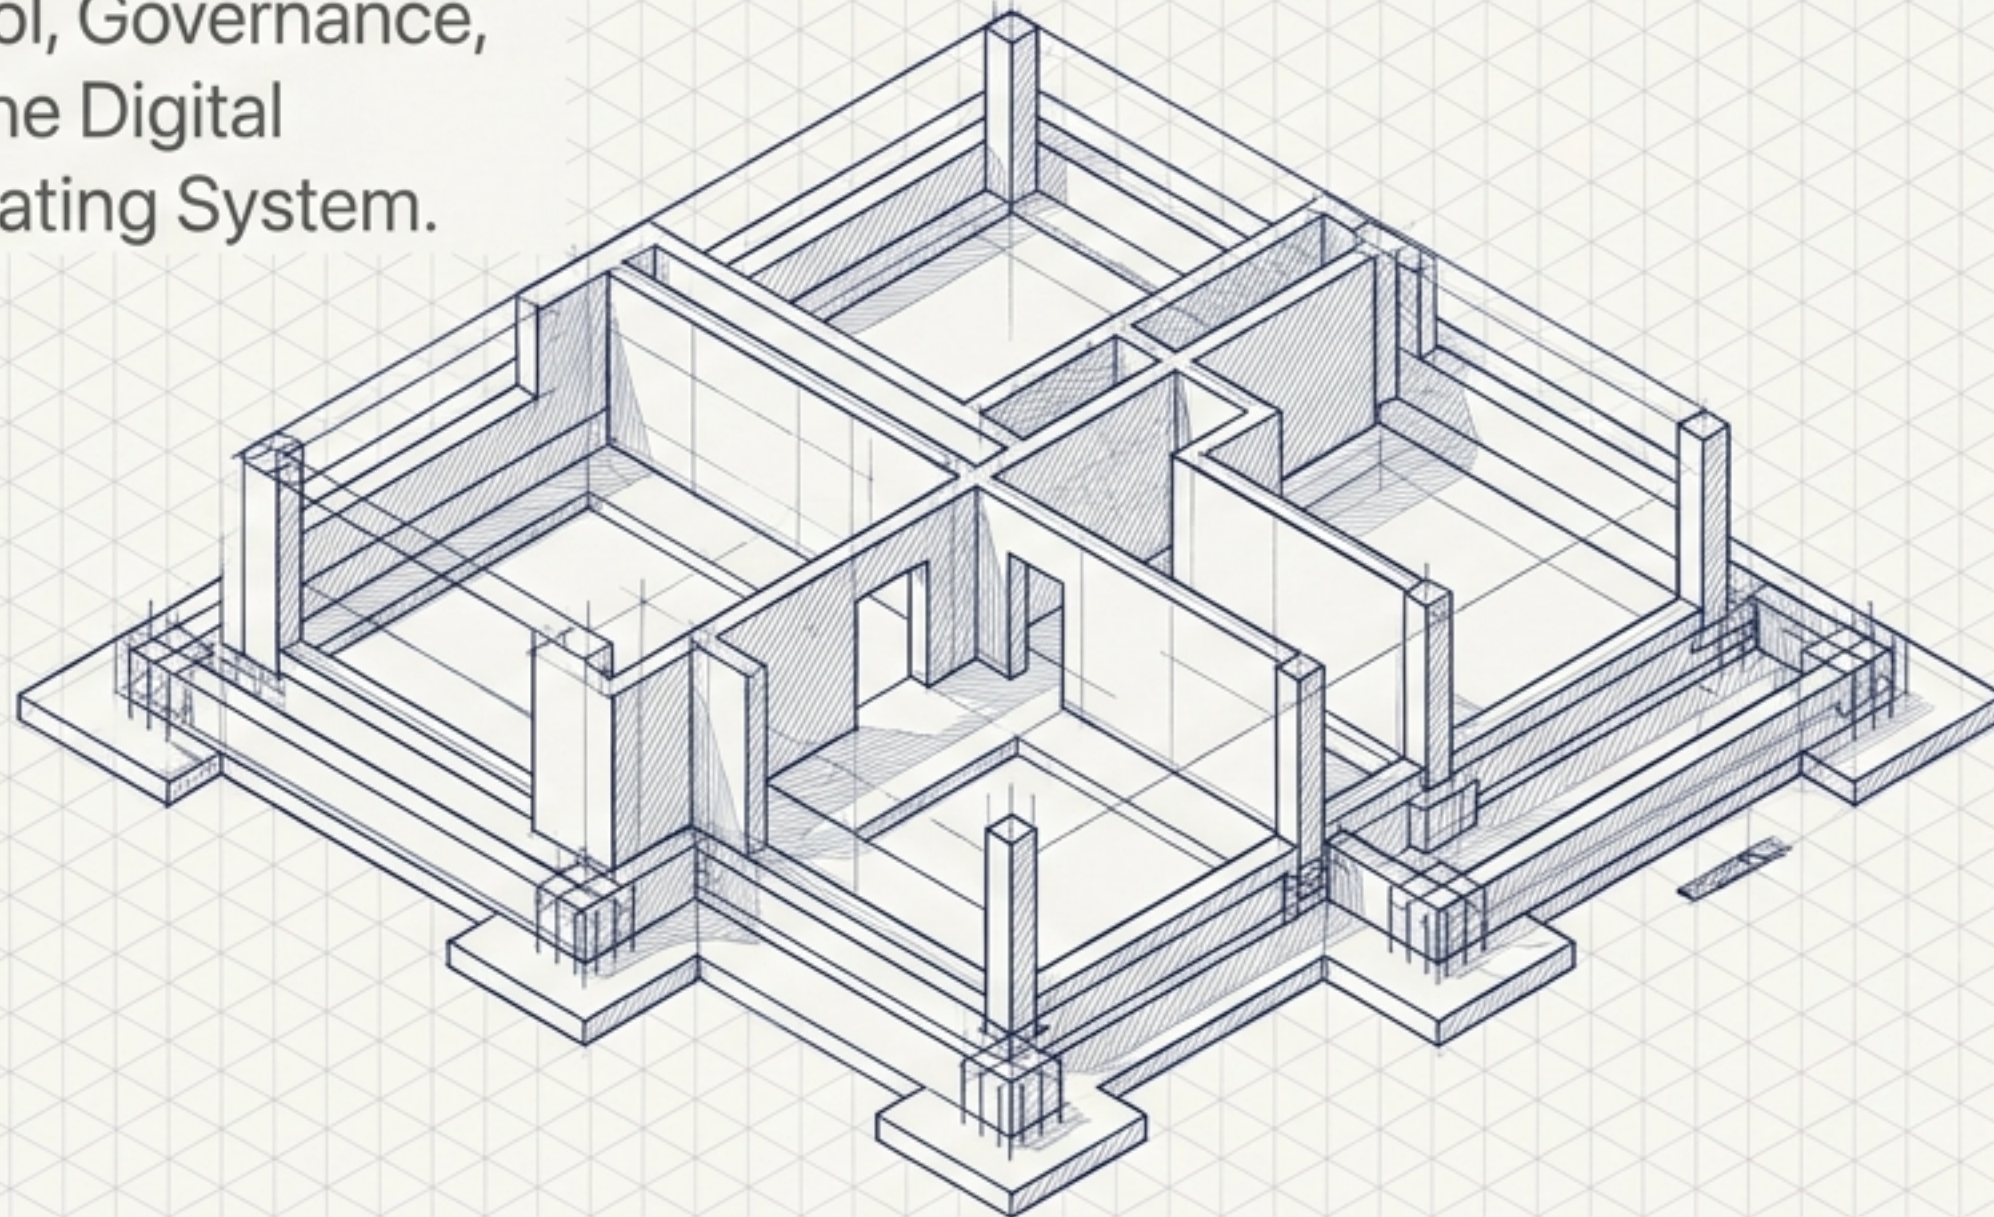


Document No:	DCOS-SOP-PS-001
Version:	1.0
Status:	APPROVED
Owner:	PMO Manager

Well-Configured Project

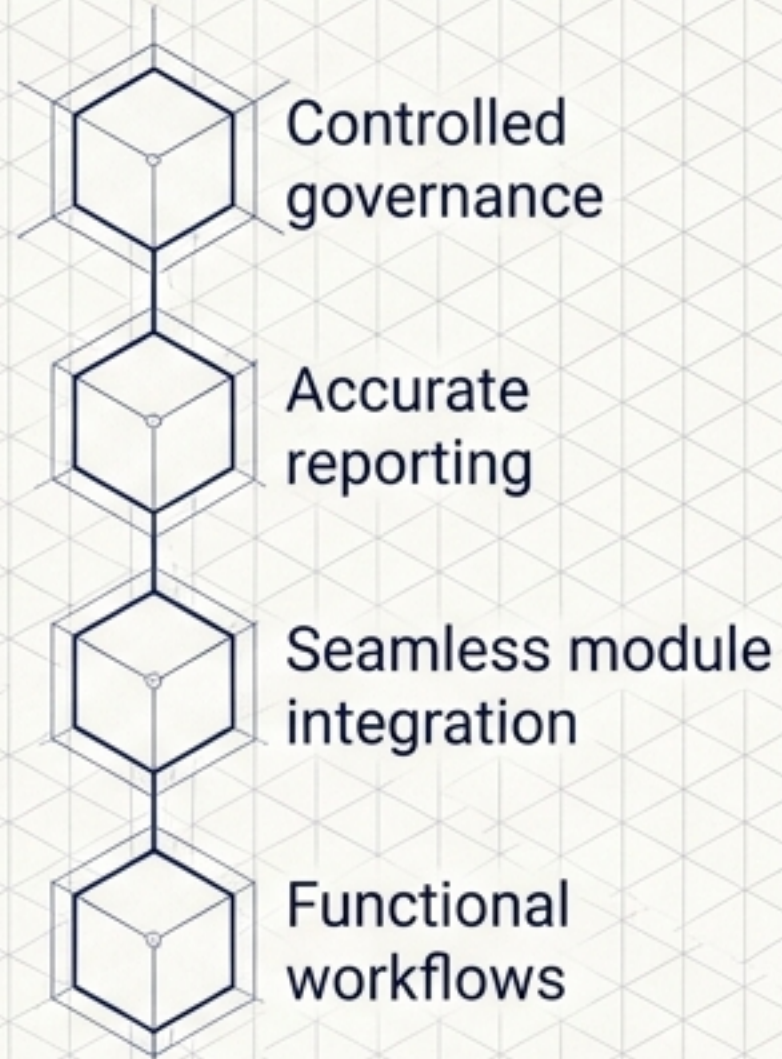


Poorly Configured Project

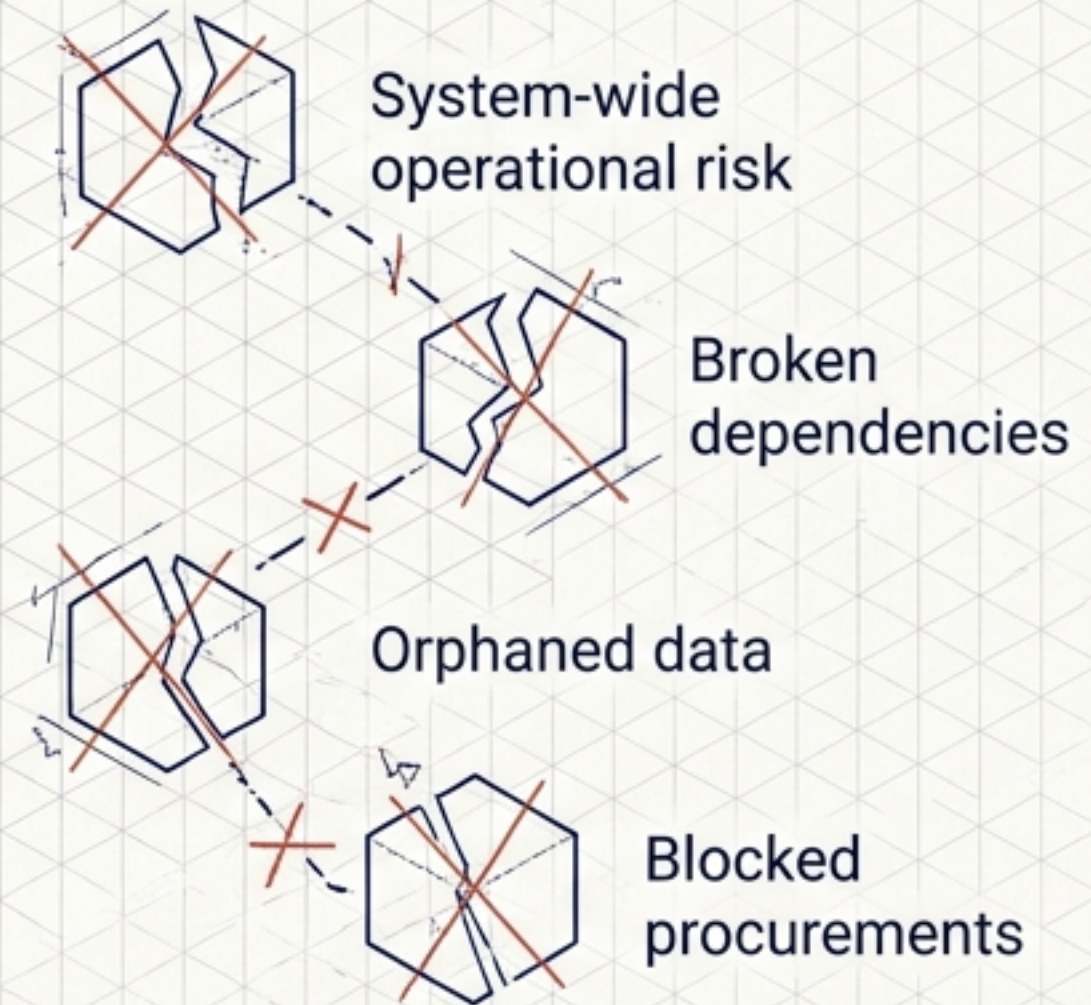


No task, document, procurement package, inspection, cost record, or report shall exist without an active project. Every DCOS module depends on Setup.

DCOS PROJECT ARCHITECTURE

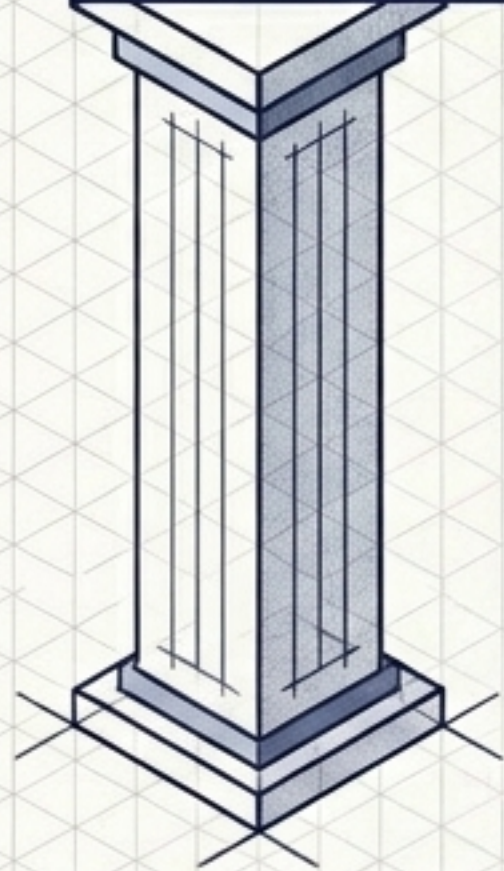


Standardization

All projects follow the exact same structural blueprint across all portfolios.

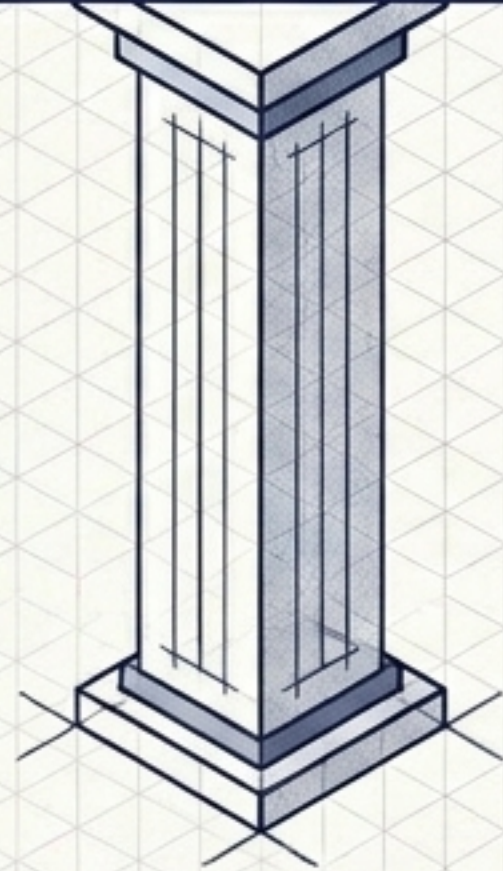


Traceability

Every project activity is heavily logged, permanently tracked, and fully auditable.



Scalability

Core architecture built to automatically support future operational growth.



Governance

Strict, unyielding control over data, access, and module permissions.



PMO Manager: The Owner

System oversight, SOP enforcement, and ultimate governance.



Project Manager: The Driver

Execution, team assignment, and primary KPI ownership.



System Administrator: The Engineer

Technical configuration, workflow routing, and backend structure.



Department Managers: The Resources

Staff provision and domain expertise allocation.

General Data

Project Name

Business Type

Industry

Contract Type

Contract Data

Key Operational Dates

Start date: _____

End date: _____

Commercial Frameworks

Payment terms: _____

Milestones: _____

Management Data

Primary Stakeholders

Client: _____

PM: _____

PM: _____


Structural Owners

Internal leads: _____

Internal leads: _____




**Project Codes are unique and mathematically standardized.
Once generated, a Project Code CANNOT be changed.**

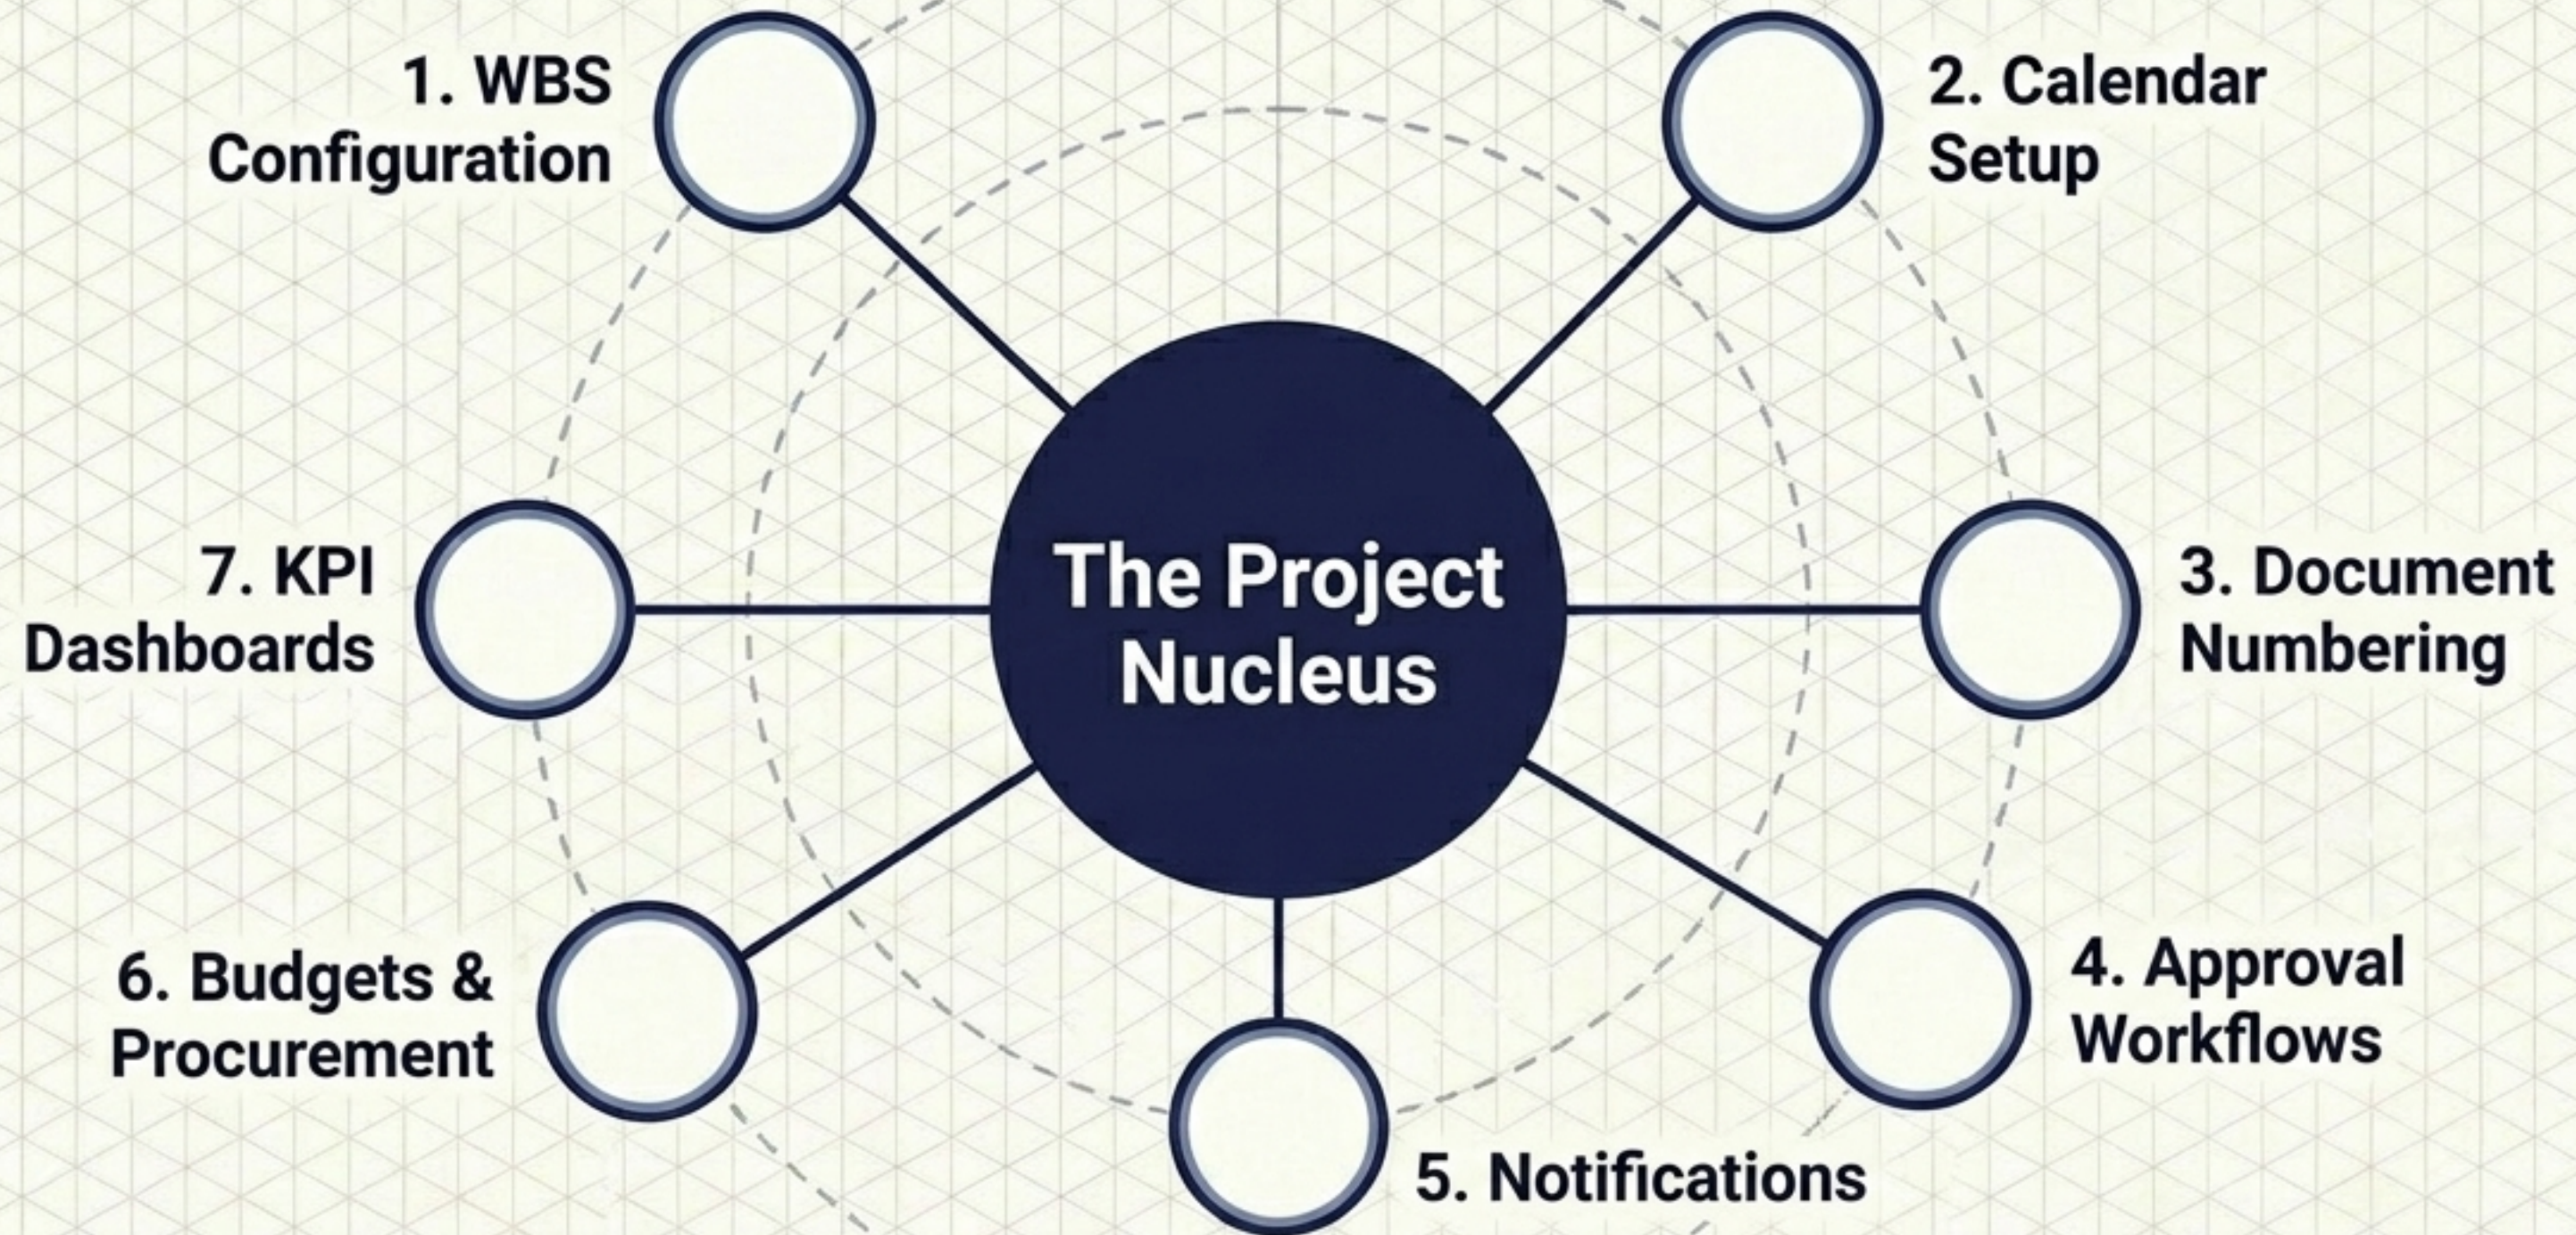


All workflows must use designated structural rules. Dashboards require precise KPI ownership before activation.

WBS Hierarchy

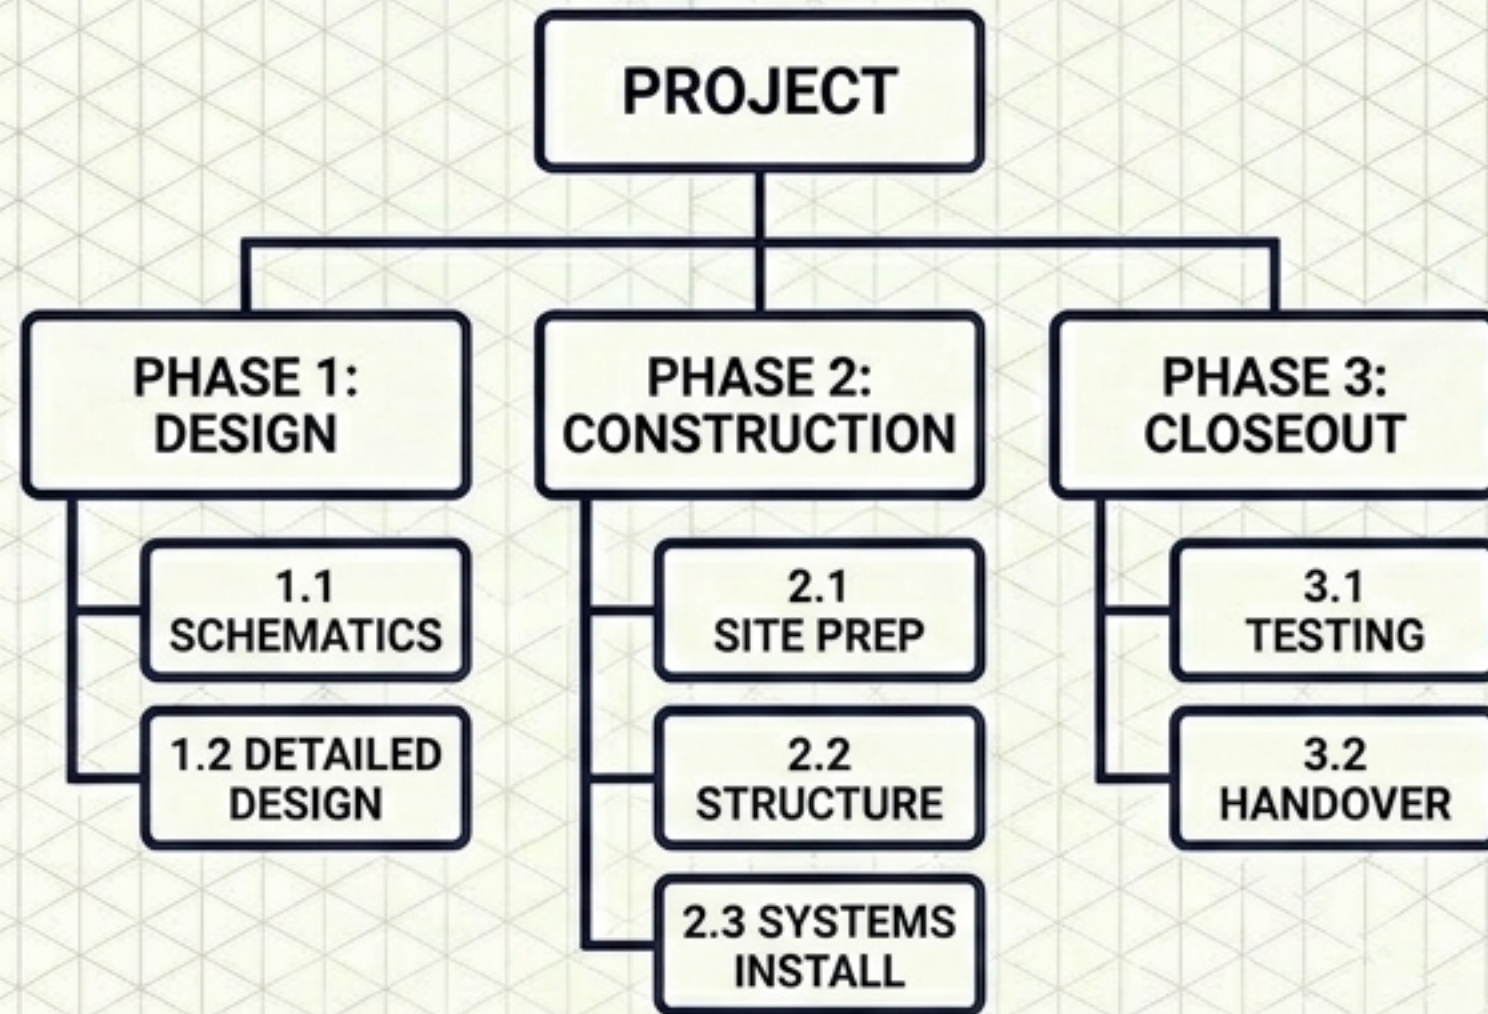

Standardized structure mandatory across all projects.

Numbering Formula

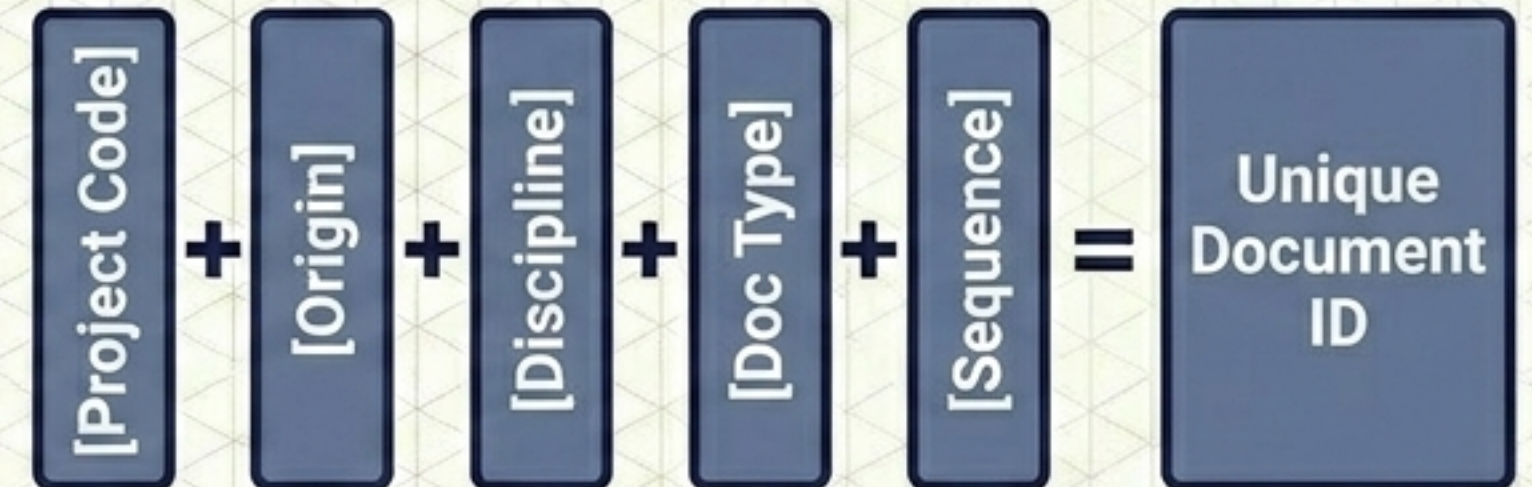


Every project must define its exact numbering syntax prior to launch.

Temporal Architecture




Project Calendar Rules: Strict definitions required for working days, working hours, project-specific holidays, and special situational calendars.

Workflow Routing

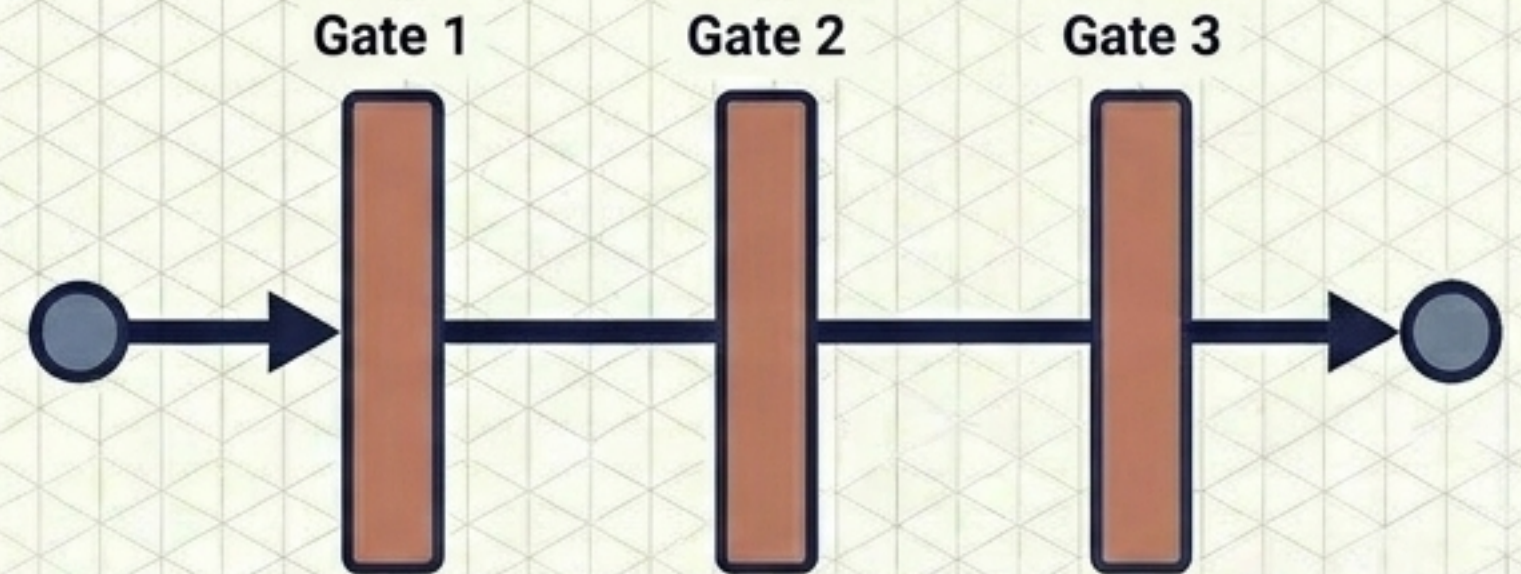

Approval Workflows & Notifications: Triggers must be configured at specific project gates. All workflows must exclusively use approved structural rules.

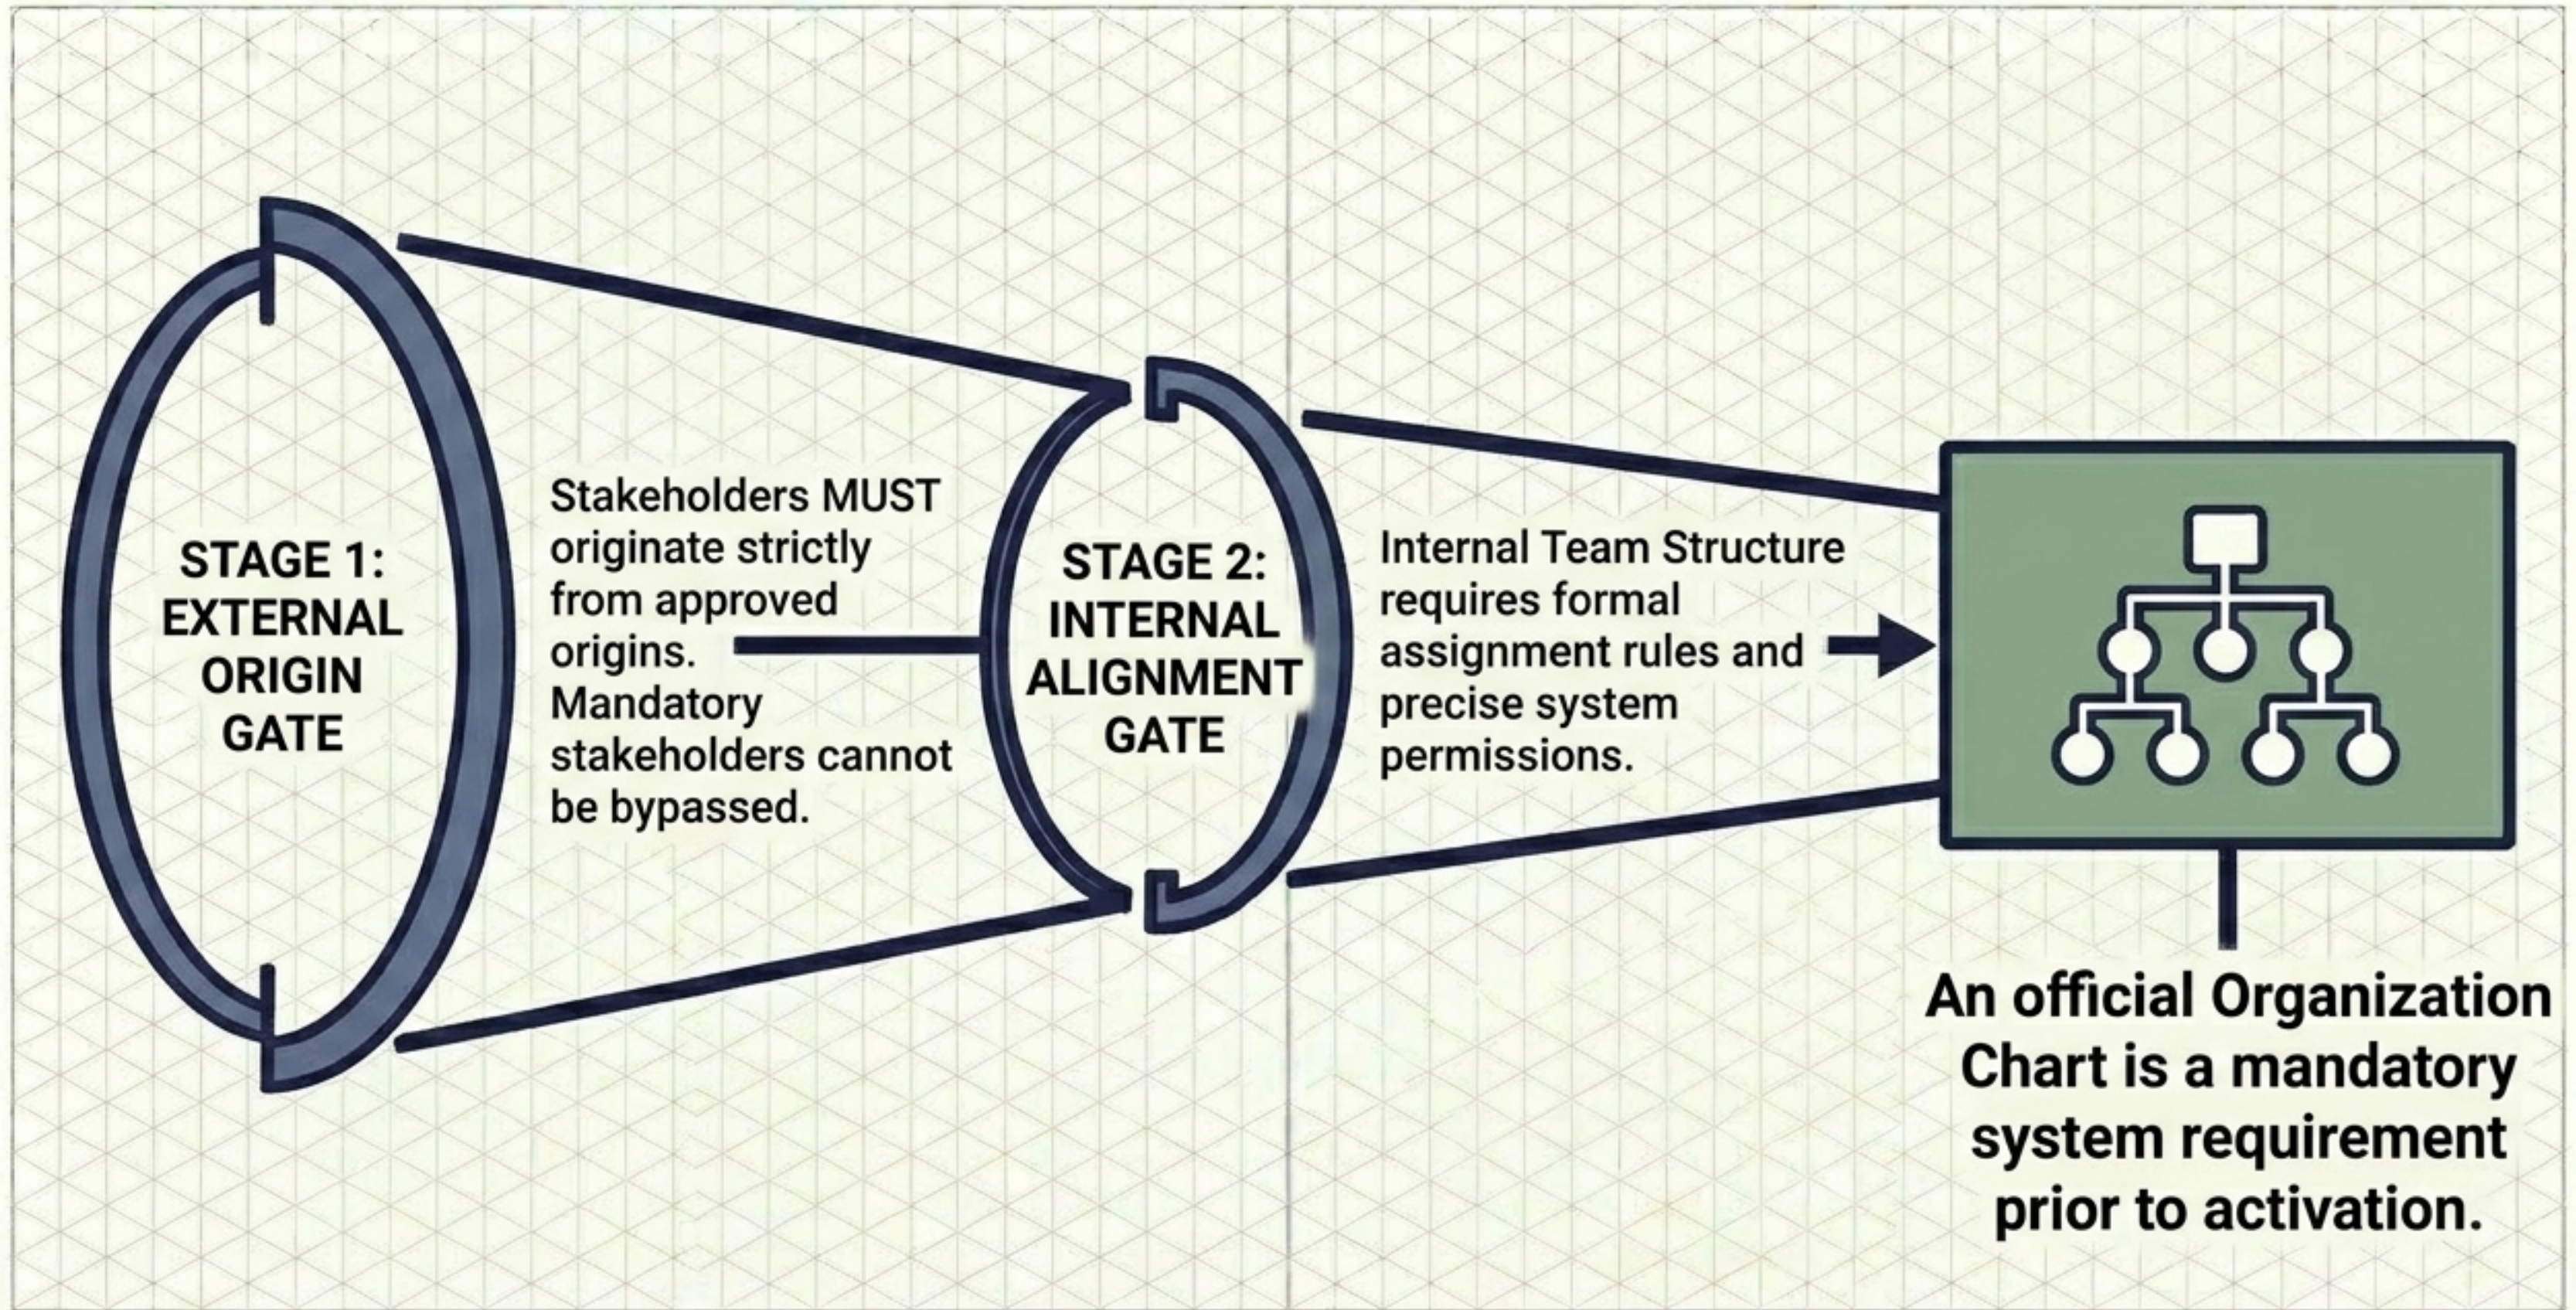


The Pre-Flight Checklist

Project Info	ON	COMPLETE
Workflows	ON	COMPLETE
Stakeholders	ON	COMPLETE
Notifications	ON	COMPLETE
Team	ON	COMPLETE
Budget	ON	COMPLETE
WBS	ON	COMPLETE
Dashboards	ON	COMPLETE
Calendar	ON	COMPLETE
Permissions	ON	COMPLETE

All 10 configuration toggles must read COMPLETE before the Activation Workflow can initiate.


Status: ACTIVE.
Live Project Environment.

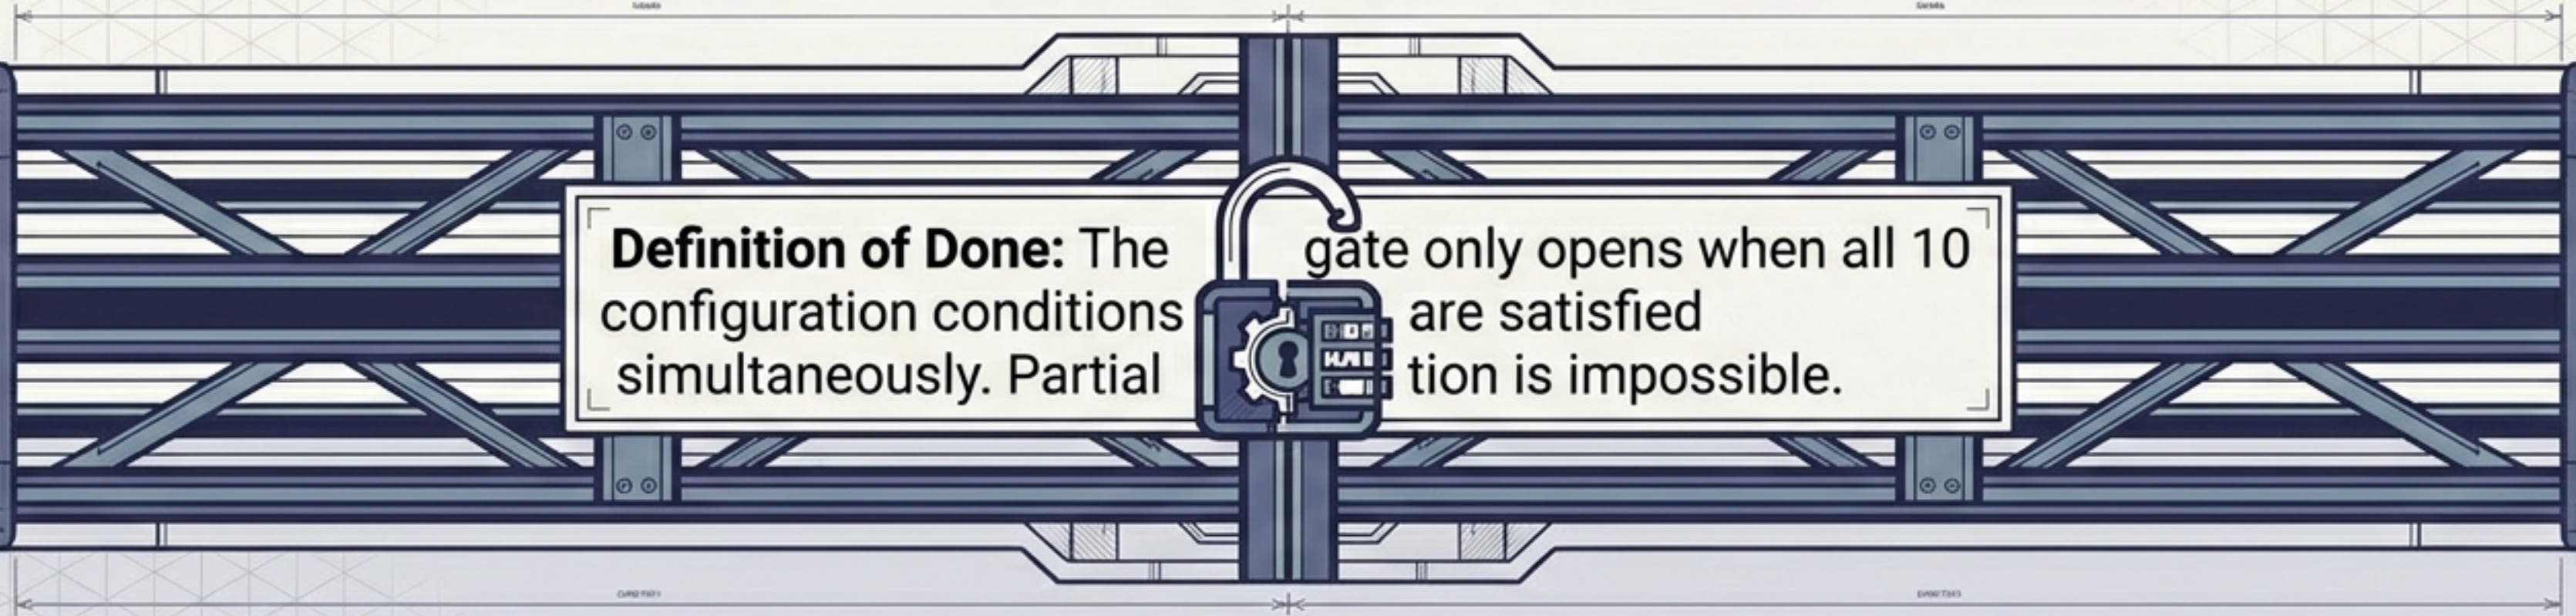


Definition of Done: The configuration conditions simultaneously. Partial

gate only opens when all 10 are satisfied
tion is impossible.


Status: DRAFT / PENDING.
Project is under setup and waiting activation.

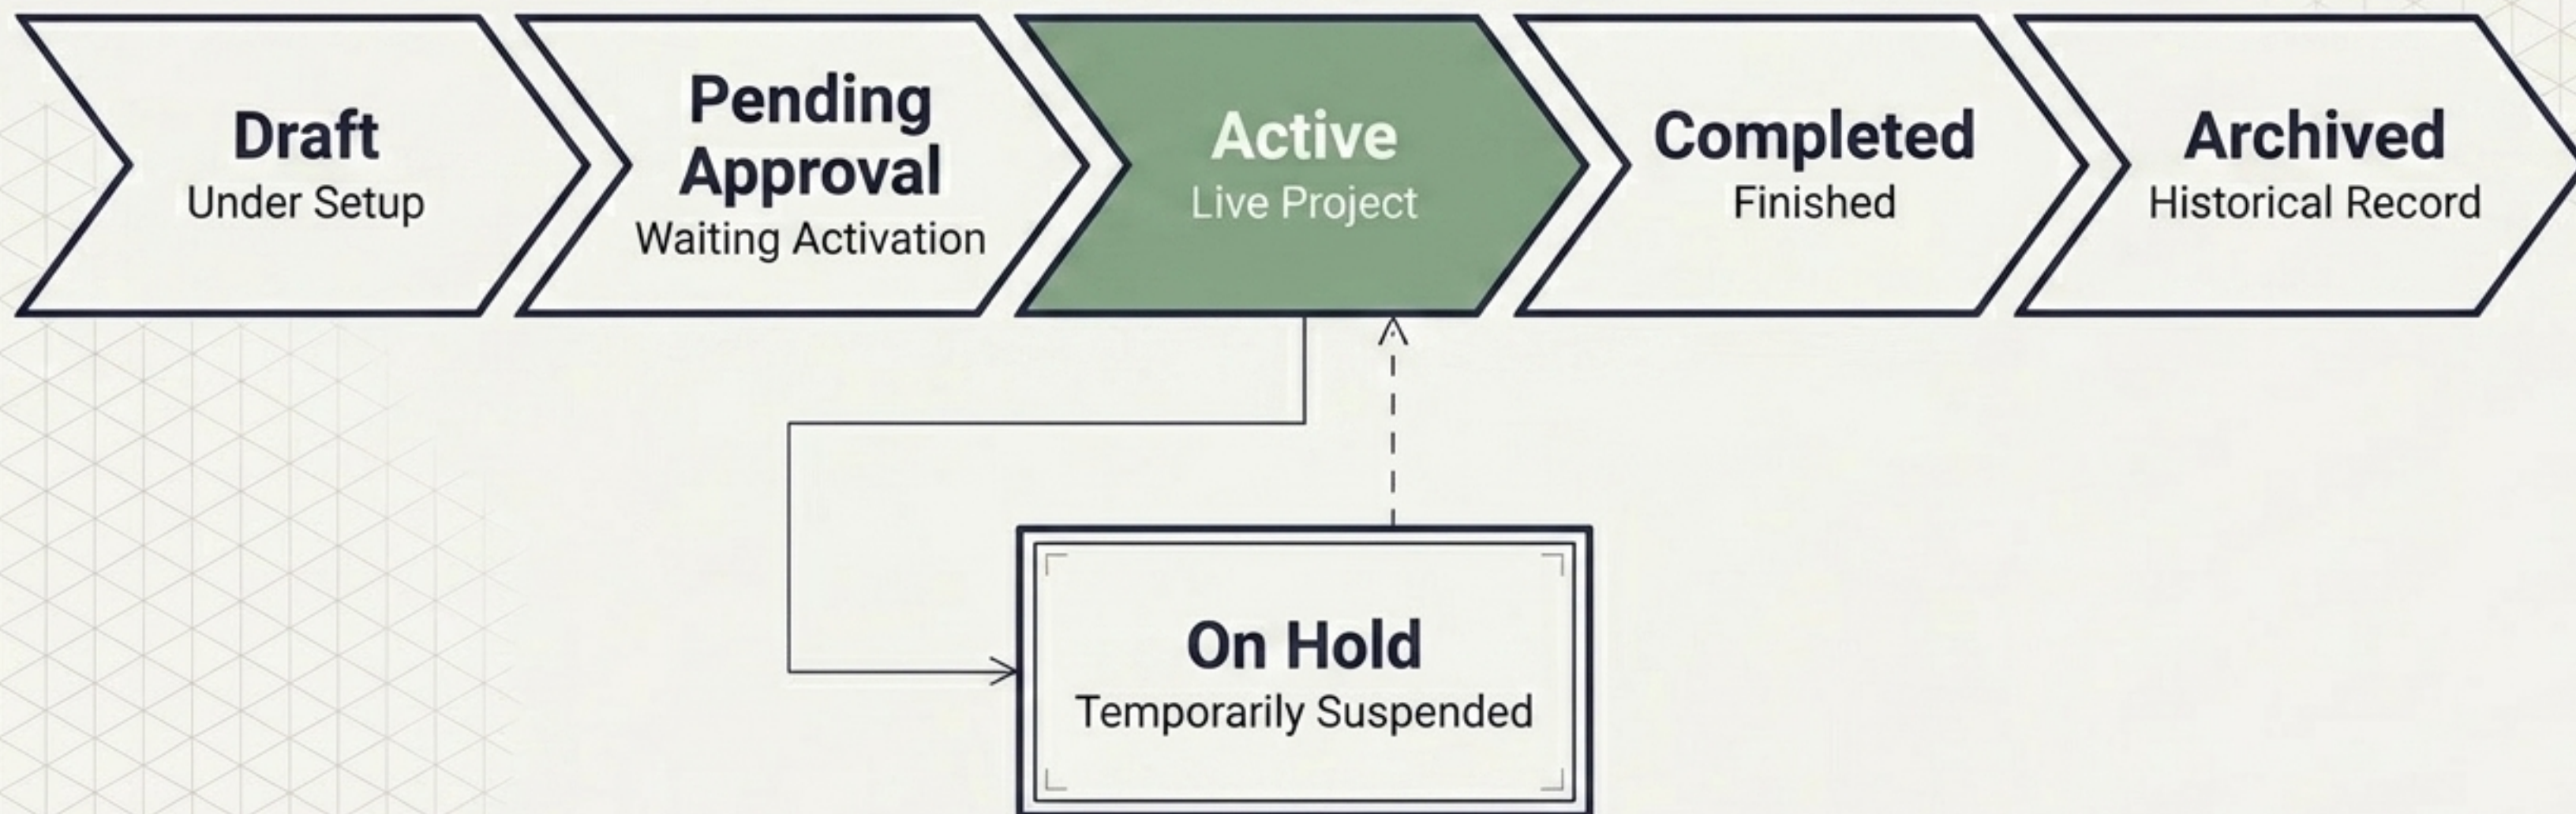




Change Management

Changes post-activation require formal, routed approval workflows.



Closure Procedure

Strict workflow dependencies must be cleared to reach 'Completed' status.



Archive & Audit

Archived projects lock down entirely. Audit logs are permanent records and mathematically cannot be deleted.



Speed (Setup Duration)

Measures time elapsed from project creation to final activation.



Volume (Completeness)

Tracks target metrics for data saturation and stakeholder assignment.



Precision (Accuracy)

Targets zero-defect configurations. Evaluates the exactness of workflows, budgets, and WBS mapping.



Project Setup is the foundation.

Every single module depends on it.
A well-configured project creates
a well-controlled ecosystem.
